GHQ/SCAP Records (RG 331, National Archives and Records Service)

Description of contents

(1) Box no. 2923

(2) Folder title/number: (19)
Packing & Crating Allocation Notice

(3) Date: Dec. 1948 - Oct. 1949

(4) Subject:

Classification	Type of record
9230, 9632	z

(5) Item description and comment:
Osaka

(6) Reproduction: (Yes) No

(7) Film no. Sheet no.

(Compiled by *National Diet Library*)

file
Alloc. Not.
Pack & crat.

HEADQUARTERS EIGHTH ARMY
United States Army
Office of the Commanding General
APO 343

18 Oct 1949

AGMGEM 386.3

SUBJECT: Additional Marking of Reparations Packages for the Philippines

TO: Commanding General
I Corps
APO 301

1. Reference is made to letter, file AGMGEM 386.3, this headquarters, subject, "Additional Marking of Reparations Packages for the Philippines", 27 September 1949.

2. The memorandum for the Reparations Board, Japanese Government (inclosure 1) is forwarded for your information and necessary action under the provisions of Operational Directive No. 51, this headquarters, 27 September 1949.

BY COMMAND OF LIEUTENANT GENERAL WALKER:

/s/t/ J. A. O'BRIEN
CWO USA
Asst Adj Gen

1 Incl.
Memo, Rep Bd, JG

DECLASSIFIED E.O. 12065 SECTION 3 (b)

BASIC: Ltr, Hq Eighth Army, AGMGEM 386.3, dtd 18 Oct 49, subj: "Additional Marking of Reparations Packages for the Philippines".

AG 004 - BA 1st Ind SD/ys

OCT 22 1949

Hq I Corps, APO 301,

TO: Chief, Tokai-hokuriku Civil Affairs Region, APO 710
Chief, Kinki Civil Affairs Region, APO 25
Chief, Chugoku Civil Affairs Region, APO 248
Chief, Shikoku Civil Affairs Region, APO 1050
Chief, Kyushu Civil Affairs Region, APO 24-5

Forwarded for your information and necessary action.

BY COMMAND OF MAJOR GENERAL COULTER:

P. L. NASH
Lt. Col. AGD
Asst Adj Gen

1 Incl:
n/c
2 copies w/d

004 2nd Ind MEB/ho

Hq Kinki Civil Affairs Region, APO 25, 25 Oct 1949

TO: Chief, Osaka Civil Affairs Team, APO 25

For your information and necessary action.

BY COMMAND OF COLONEL O'MOHUNDRO:

GEORGE MINARIK
Captain CE
Adjutant

1 Incl
n/c

OSAKA M.G.
RES-COM-IND
FILE 1-6009

10637C

GENERAL HEADQUARTERS
SUPREME COMMANDER FOR THE ALLIED POWERS
CIVIL PROPERTY CUSTODIAN

387.6 (22 Sep 49)CPC/RP   13 October 1949

MEMORANDUM FOR: REPARATIONS BOARD, JAPANESE GOVERNMENT

SUBJECT: Additional Marking of Reparations Packages for the Philippines

1. Reference is made to memorandum for the Japanese Government, file 387.6 (22 Sep 49)CPC/RP, 22 September 1949, subject, "Additional Marking of Reparations Packages for the Philippines," from General Headquarters, Supreme Commander for the Allied Powers.

2. In the event that items listed in memorandum reference 1 above, have been included in packages with items not listed and packages have been completed, packages will be marked "MANILA" only.

3. Packages at port that contain only items listed in memorandum reference 1 above, will be marked "SHIPYARD" in addition to destination "MANILA."

E. C. Miller Jr.

E. C. MILLER, Jr
Colonel, Infantry
Deputy Custodian

Kinko

Incl 1

file
alloc. not
pack d cust

HEADQUARTERS EIGHTH ARMY
United States Army
Office of the Commanding General
APO 343

Oct 11 1949

AGMGEM 386.3

SUBJECT: Loading Operations of Scheduled Vessels to Lift Reparations Cargo

TO: Commanding General
I Corps
APO 301

1. Reference is made to paragraph IV, d. (1) Circular 19, General Headquarters, Supreme Commander for the Allied Powers, 23 June 1948.

2. Port operations incident to the loading of ships, scheduled to lift reparations cargo, such as loading of lighters, will not commence until notification is received, by telephone from this headquarters, as to the exact time of arrival of the scheduled vessel. It is the responsibility of the local Civil Affairs Team to notify the Japanese authorities when to commence loading operations.

3. In the event ships are scheduled to lift reparations cargo at more than one port, it is requested that the Civil Affairs Team notify the Civil Affairs Team at the next port to be visited when the ship can be expected to arrive. Notification should be made as soon as possible and not later than 48 hours before arrival at next scheduled port.

4. Each recipient nation has been informed that it is the desire of General Headquarters, Supreme Commander for the Allied Powers, that the shipping agent and the ship's master consult with the local Civil Affairs Team regarding all matters pertaining to the loading of reparations cargo.

5. It is believed that such coordination will expedite loading operations in the future and eliminate unnecessary expenses.

BY COMMAND OF LIEUTENANT GENERAL WALKER:

/s/t/ J. A. O'BRIEN
CWO USA
Asst Adj Gen

BASIC: Ltr, Hq Eighth Army, AGMGEM 386.3, dtd 11 Oct 49, subj: "Loading Operations of Scheduled Vessels to Lift Reparations Cargo".

AG 386.3 - BA 1st Ind SD/ys

Hq I Corps, APO 301. OCT 15 1949

TO: Chief, Tokai-hokuriku Civil Affairs Region, APO 710
Chief, Kinki Civil Affairs Region, APO 25
Chief, Chugoku Civil Affairs Region, APO 248
Chief, Shikoku Civil Affairs Region, APO 1050
Chief, Kyushu Civil Affairs Region, APO 24-5

Forwarded for your information and necessary action.

BY COMMAND OF MAJOR GENERAL COULTER:

P. L. NASH
Lt. Col. AGD
Asst Adj Gen

RECORDED

004 2nd Ind MEB/ho

Hq Kinki Civil Affairs Region, APO 25, 17 Oct 1949

TO: Chief, Osaka Civil Affairs Team, APO 25
Chief, Hyogo Civil Affairs Team, APO 317

Forwarded for your information and necessary action.

BY ORDER OF COLONEL O'MOHUNDRO:

GEORGE MINARIK
Captain CE
Adjutant

OSAKA A.G
RES-COM-IND
FILE 1986
10803C

10/907

BASIC: Ltr, Hq Eighth Army, AGMGEM 386.3, dtd 11 Oct 49, subj: "Loading Operations of Scheduled Vessels to Lift Reparations Cargo".

AG 386.3 - BA 1st Ind SD/ys

Hq I Corps, APO 301,

OCT 15 1949

TO: Chief, Tokai-hokuriku Civil Affairs Region, APO 710
Chief, Kinki Civil Affairs Region, APO 25
Chief, Chugoku Civil Affairs Region, APO 248
Chief, Shikoku Civil Affairs Region, APO 1050
Chief, Kyushu Civil Affairs Region, APO 24-5

Forwarded for your information and necessary action.

BY COMMAND OF MAJOR GENERAL COULTER:

P. L. NASH
Lt. Col. AGD
Asst Adj Gen

RECORDED

004 2nd Ind MEB/ho

Hq Kinki Civil Affairs Region, APO 25, 17 Oct 1949

TO: Chief, Osaka Civil Affairs Team, APO 25
Chief, Hyogo Civil Affairs Team, APO 317

Forwarded for your information and necessary action.

BY ORDER OF COLONEL O'MOHUNDRO:

GEORGE MINARIK
Captain CE
Adjutant

OSAKA A.G
RES-COM-IND
FILE 1986
5
10803C

10/907

Packaging & Crating
Allocation Notices

HEADQUARTERS
OSAKA CIVIL AFFAIRS TEAM
APO 25

29 October 1949

MEMORANDUM FOR: Osaka Finance Office

THROUGH: Kinki Liaison Office

SUBJECT: Packaging and Crating Operations

1. Refer to the following applications from your office, copies inclosed herewith:

a. File OFO No. 61, KLO file KKLCO No. 872 ER, regarding corrections to tonnage packaged and crated in connection with Allocation Notice 1-54 (Incl No. 1).

b. File OFO No. 62, KLO file KKLCO No. 871 ER, regarding corrections to tonnage packaged and crated in connection with Allocation Notice 1-54 (Incl No. 2).

c. File OFO No. 58, KLO file KKLCO No. 868 ER, regarding corrections to tonnages required to be packaged and crated in connection with Allocation Notices 1-69 and 4-63 (Incl No. 3).

2. Records of this headquarters indicate that:

a. Weight of the crated items cited in reference 1a above totalled 209.765 m/t.

b. Weight of the crated trackage cited in reference 1b above totalled 313.504 m/t.

3. It is required that the eighty-six (86) iron weights, totalling 184.8 m/t, be crated for shipment with the allocated water accumulaters in which the weights are located, cite paragraph 2 of your letter, reference 1c above.

4. Investigation by this headquarters confirms the total weight of the 198 items crated for Allocation Notice 4-63, cite paragraph 3 of your letter reference 1c above, to be 993.824 m/t.

FOR THE CHIEF:

3 Incls:
as above

FRED N. ALEXANDER
WOJC USA
Asst Adjutant

OS
RI
FI 0-5960

Packaging & Crating
Allocation Notices

HEADQUARTERS
OSAKA CIVIL AFFAIRS TEAM
APO 25

28 October 1949

SUBJECT: Transmittal of Progress Reports and Packing Lists

TO: General Headquarters
Supreme Commander for the Allied Powers
APO 500
ATTN: Civil Property Custodian

1. Herewith transmitted are progress reports for the period 8 October thru 15 October regarding Allocation Notices 1-68, 1-69, 2-61, 3-60, 3-61, 4-63 and 4-65, and packing lists for the 183 packages indicated in the reports as having been completed in the reported period.

2. The progress reports and packing lists, prepared by the Osaka Finance Division, have been reviewed by this headquarters and found to be accurately reflective of the status of operations.

FOR THE CHIEF:

12 Incls:
1 thru 7: progress reports (ea dup) for AN's 1-68,1-69,2-61,3-60, 3-61,4-63 & 4-65
8 thru 12: Packing lists (ea trip) for AN's 1-68,1-69,3-60,4-63 & 4-65

FRED N. ALEXANDER
WOJG USA
Asst Adjutant

OSAKA M.G.
RES-COM-IND
FILE 0-2659

DAILY REPORT ON COMPLETION OF PAC

RECIPIENT NATION	ALLOCATION NO.	DESTINATION	PACKAGES COMPLETED				NO. OF PACKAGE
			NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	
CHINA	1-68	KEELUNG	44	83,410	208.5	183,879	605
	1-69	"	17	27,036	67.8	59,796	49
	TOTAL		61	110,446	276.3	243,675	654
NETHER-LAND	2-60	SOURABAYA	0	0	0	0	14
		BATAVIA	0	0	0	0	59
	SUB - TOTAL		0	0	0	0	73
	2-61	BATAVIA	0	0	0	0	108
	TOTAL		0	0	0	0	181
PHILIPPINE	3-60	MANILA	22	74,435	65.8	58,024	560
		MANILA SHIPYARD	0	0	0	0	0
	SUB - TOTAL		22	74,435	65.8	58,024	560
	3-61	MANILA	23	33,930	75.7 ~~75.7~~	66,757	24
		MANILA SHIPYARD	0	0	0	0	0
	SUB - TOTAL		23	33,930	75.7	66,757	24
	TOTAL		45	108,365	141.5	124,781	584
UNITED KINGDOOM	4-63	RANGOON	0	0	0	0	145
		HONG KONG	28	87,850	204.2	180,094	28
		PENANG	2	20,340	53.3	47,010	187
		JESSELTON	0	0	0	0	6
		SINGAPORE	0	0	0	0	19
	SUB - TOTAL		30	108,190	257.5	227,104	385
	4-65	RANGOON	0	0	0	0	8
		HONG KONG	0	0	0	0	0
		PENANG	0	0	0	0	8
		JESSELTON	0	0	0	0	0
		SINGAPORE	0	0	0	0	0
	SUB - TOTAL		0	0	0 ~~257.5~~	0	16
	TOTAL		30	108,190	257.5	227,104	401
GRAND TOTAL			136	327,001	675.3	595,560	1,820

COMPLETION OF PACKAGES BY DESTINATIONS

NO. 1
DATE 4th. Oct

ES COMPLETED			TOTAL PACKAGES COMPLETED TO DATE				REMARKS
VT.	GROSS VOL.	MEAS. TON.	NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON.	
10	208.5	183,879	605	1.263,521	3,528,6	3.112,346	
36	67.8	59,796	49	112,754	219.6	193,672	
46	276.3	243,675	654	1.376,275	3,748,2	3.306,018	
	0	0	14	16,392	38.9	34,320	
	0	0	59	24,587	15.6	13,735	
	0	0	73	40,979	54.5	48,055	
	0	0	108	230,103	618.1	545,211	
	0	0	181	271,082	672.6	593,266	
35	65.8	58,024	560	1.844,690	3,673.8	3,236,333	
	0	0	0	0	0	0	
35	65.8	58,024	560	1.844,690	3,673.8	3.236,333	
20	75.7 ~~65.7~~	66,757	24	35,381	78.7	69,403	
	0	0	0	0	0	0	
0	75.7	66,757	24	35,381	78.7	69,403	
5	141.5	124781	584	1.880,071	3,752.5	3.305,736	
	0	0	145	337,961	1,082.0	954,293	
0	204.2	180,094	28	87,850	204.2	180,094	
0	53.3	47,010	187	1.489,558	1,791.4	1.579,973	
	0	0	6	31,780	173.0	152,585	
	0	0	19	66,488	206.1	181,784	
0	257.5	227,104	385	2.013,637	3,456.7	3.048,729	
	0	0	8	7,870	13.4	11,815	
	0	0	0	0	0	0	
	0	0	8	49,230	68.3	60,238	
	0	0	0	0	0	0	
	0	0	0	0	0	0	
	0 ~~249~~	0	16	57,100	81.7	72,053	
0	257.5	227,104	401	2.070,737	3,538.4	3.120,782	
1	675.3	595,560	1,820	5.598,165	11,711.7	10.325,802	

DAILY REPORT ON COMPLETION OF PACKA

RECIPIENT NATION	ALLOCATION NO.	DESTINATION	PACKAGES COMPLETED				TOTA	
			NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	NO. OF PACKAGE	GRO
CHINA	1-68	KEELUNG					605	1.2
	1-69	"					49	
	TOTAL						654	1.3
NETHER-LAND	2-60	SOURABAYA					14	
		BATAVIA					59	
	SUB-TOTAL						73	
	2-61	BATAVIA					108	
	TOTAL						181	
PHILIPPINE	3-60	MANILA					560	1.8
		MANILA SHIPYARD					0	
	SUB-TOTAL						560	1.8
	3-61	MANILA					24	
		MANILA SHIPYARD					0	
	SUB-TOTAL						24	
	TOTAL						584	1.88
UNITED KINGDOOMM	4-63	RANGOON					145	33
		HONG KONG					28	8
		PENANG					187	1.48
		JESSELTON					6	3
		SINGAPORE					19	
	SUB-TOTAL						385	2.01
	4-65	RANGOON					8	
		HONGKONG					0	
		PENANG					8	4
		JESSELTON					0	
		SINGAPORE					0	
	SUB-TOTAL						16	5
	TOTAL						401	2.07
GRAND TOTAL							1.820	5.59

COMPLETION OF PACKAGES BY DESTINATIONS

NO. 2

DATE 5th. Oct.

S COMPLETED		TOTAL PACKAGES COMPLETED TO DATE				REMARKS
GROSS VOL.	MEAS. TON	NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON.	
		605	1.263,521	3,528.6	3.112,346	
		49	112,754	219.6	193,672	
		654	1.376,275	3,748.2	3.306,018	
		14	16,392	38.9	34,320	
		59	24,587	15.6	13,735	
		73	40,979	54.5	48,055	
		108	230,103	618.1	545,211	
		181	271.082	672.6	593,266	
		560	1.844,690	3,673.8	3.236,333	
		0	0	0	0	
		560	1.844,690	3,673.8	3.236,333	
		24	35,381	78.7	69,403	
		0	0	0	0	
		24	35,381	78.7	69,403	
		584	1.880,071	3,752.5	3.305,736	
		145	337,961	1,082.0	954,293	
		28	87,850	204.2	180,094	
		187	1.489,558	1,791.4	1.579,973	
		6	31,780	173.0	152,585	
		19	66,488	206.1	181,784	
		385	2.013,637	3,456.7	3.048,729	
		8	7.870	13.4	11,815	
		0	0	0	0	
		8	49,230	68.3	60,238	
		0	0	0	0	
		0	0	0	0	
		16	57,100	81.7	72,053	
		401	2.070,737	3,538.4	3.120,782	
		1.820	5.598,165	11,711.7	10.325,802	

DAILY REPORT ON COMPLETION OF PACKAG

RECIPIENT NATION	ALLOCATION NO.	DESTINATION	PACKAGES COMPLETED				TOTAL	
			NO. OF PACKAGE	GROSS WT.	GROSS VOL. MEAS. TON		NO. OF PACKAGE	GROS
CHINA	1-68	KEELUNG	2	11,240	23.0	20,285	607	1.2
	1-69	"	0	0	0	0	49	
	TOTAL		2	11,240	23.0	20,285	656	1.3
NETHER-LAND	2-60	SOURABAYA					14	
		BATAVIA					59	
	SUB-TOTAL						73	
	2-61	BATAVIA					108	
	TOTAL						181	
PHILIPPINE	3-60	MANILA					560	1.8
		MANILA SHIPYARD					0	
	SUB-TOTAL						560	1.8
	3-61	MANILA					24	
		MANILA SHIPYARD					0	
	SUB-TOTAL						24	
	TOTAL						584	1.8
UNITED KINGDOOM	4-63	RANGOON	5	7,705	34.5	30,424	150	
		HONG KONG					28	
		PENANG					187	1.4
		JESSELTON					6	
		SINGAPORE	6	50,956	213.1	187,953	25	
	SUB-TOTAL		11	58,661	247.6	218,379	396	2.0
	4-65	RANGOON	7	20,270	33.8	29,809	15	
		HONGKONG	0	0	0	0	0	
		PENANG	83	827,160	1,030.8	909,133	91	8
		JESSELTON	0	0	0	0	0	
		SINGAPORE	0	0	0	0	0	
	SUB-TOTAL		90	847,430	1,064.6	938,942	106	1
	TOTAL		101	906,091	1,312.2	1,157,321	502	2.9
GRAND TOTAL			103	917,331	1,335.2	1,177,606	1,923	6.5

COMPLETION OF PACKAGES BY DESTINATIONS

NO. 3

DATE 6th. oct.

GES COMPLETED			TOTAL PACKAGES COMPLETED TO DATE				REMARKS
WT.	GROSS VOL.	MEAS. TON	NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	
40	23.0	20,285	607	1.274,761	3,551.6	3.132,631	
0	0	0	49	112,744	219.6	193,672	
40	23.0	20,285	656	1.382,515	3.771.2	3.326,303	
			14	16,392	38.9	34,32	
			59	24,587	15.6	13,735	
			73	40,979	54.5	48,055	
			108	230,103	618.1	545,211	
			181	271,082	672.6	593,266	
			560	1.844,690	3,673.8	3.236,333	
			0	0	0	0	
			560	1.844,690	3,673.8	3.236,333	
			24	35,381	78.7	69,403	
			0	0	0	0	
			24	35,381	28.7	69,403	
			584	1.880,071	3,752.5	3.305,736	
25	34.5	30,425	150	345,666	1.116.5	984,719	
			28	87,850	204.2	180,094	
			187	1.489,558	1,291.4	1.579,973	
			6	31,780	173.0	152,585	
46	213.1	187,953	25	117,444	419.2	369,737	
61	247.6	218,379	396	2.072,298	3,704.3	3.267,108	
20	33.8	29,809	15	28,140	47.2	41,674	
0	0	0	0	0	0	0	
60	1,030.8	909,133	91	876,390	1,099.1	969,371	
0	0	0	0	0	0	0	
0	0	0	0	0	0	0	
430	1,064.6	938,942	106	904,530	1,146.3	1.010,995	
091	1,312.2	1.157,371	502	2.976,828	4,850.6	4.278,103	
331	1.335.2	1.177,606	1.923	6.515,496	13.046.9	11.503,408	

DAILY REPORT ON COMPLETION OF PACKA

RECIPIENT NATION	ALLOCATION NO.	DESTINATION	PACKAGES COMPLETED				TOTA	
			NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	NO. OF PACKAGE	GROS
CHINA	1-68	KEELUNG	141	243,795	750.2	661.619	248	1.5
	1-69	"	0	0	0	0	49	
	TOTAL		141	243,795	750.2	661.619	297	1.6
NETHER-LAND	2-60	SOURABAYA					14	
		BATAVIA					59	
	SUB-TOTAL						73	
	2-61	BATAVIA					108	
	TOTAL						181	
PHILIPPINE	3-60	MANILA					560	1.7
		MANILA SHIPYARD					0	
	SUB-TOTAL						560	1.7
	3-61	MANILA	3	2,620	5.0	4,409	27	
		MANILA SHIPYARD	1	630	1.4	1,234	1	
	SUB-TOTAL		4	3,250	6.4	5,643	28	
	TOTAL		4	3,250	6.4	5,643	588	1.8
UNITED KINGDOOM	4-63	RANGOON					150	3
		HONG KONG					28	
		PENANG					187	1.9
		JESSELTON					6	
		SINGAPORE					25	1
	SUB-TOTAL						396	2.0
	4-65	RANGOON					15	
		HONGKONG					5	
		PENANG					91	8
		JESSELTON					0	
		SINGAPORE					0	
	SUB-TOTAL						106	9
	TOTAL						502	2.9
GRAND TOTAL			145	247,045	756.4	667,242	2,068	6.7

COMPLETION OF PACKAGES BY DESTINATIONS

NO. 4

DATE 7th. oct.

GES COMPLETED			TOTAL PACKAGES COMPLETED TO DATE				REMARKS
WT.	GROSS VOL.	MEAS. TON	NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	
95	70.2	41,619	248	1,518,546	4,301.8	3,724,250	
0	0	0	49	112,764	211.6	183,672	
95	70.2	41,619	297	1,631,310	4,521.4	3,787,922	
			14	14,392	38.9	34,320	
			59	24,587	151	13,735	
			23	46,979	54.5	48,055	
			108	230,103	418.1	345,211	
			181	324,082	672.5	593,241	
			510	1,844,190	3,173.8	3,236,333	
			0	0	0	0	
			510	1,844,190	3,173.8	3,236,333	
20	5.0	4,409	27	38,001	83.7	73,812	
30	1.4	1,234	1	530	1.4	1,234	
50	6.4	5,643	28	38,531	85.1	75,046	
50	6.4	5,643	588	1,883,371	3,258.9	3,311,379	
			150	345,166	1,116.5	984,719	
			28	87,850	204.2	180,094	
			187	1,489,558	1,791.4	1,579,973	
			6	31,780	173.0	152,585	
			25	117,444	419.2	361,737	
			396	2,072,298	3,704.3	3,267,108	
			15	28,140	47.2	41,634	
			0	0	0	0	
			91	826,390	1,099.1	969,371	
			0	0	0	0	
			0	0	0	0	
			104	904,530	1,141.3	1,010,995	
			502	2,976,828	4,850.6	4,278,103	
25	76.1	47,242	2,068	6,742,541	13,803.5	12,170,670	

DECLASSIFIED E.O. 12065 SECTION 3 (E), NARS DATE

DAILY REPORT ON COMPLETION OF PACKAGE

RECIPIENT NATION	ALLOCATION NO.	DESTINATION	PACKAGES COMPLETED				TOTAL P	
			NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON.	NO. OF PACKAGE	GROSS W
CHINA	1-68	KEELUNG					748	1.518,5
	1-69	"					49	112,7
	TOTAL						797	1.631,3
NETHER-LAND	2-60	SOURABAYA					14	16,3
		BATAVIA					59	24,5
	SUB-TOTAL						73	40,9
	2-61	BATAVIA					108	230,1
	TOTAL						181	271,0
PHILIPPINE	3-60	MANILA					560	1.844,6
		MANILA SHIPYARD					0	
	SUB-TOTAL						560	1.844,6
	3-61	MANILA					27	38,0
		MANILA SHIPYARD					1	6
	SUB-TOTAL						28	38,6
	TOTAL						588	1.883,3
UNITED KINGDOOM	4-63	RANGOON					150	345,6
		HONG KONG					28	87,8
		PENANG					187	1.489,5
		JESSELTON					6	31,7
		SINGAPORE					25	117,4
	SUB-TOTAL						396	2.072,2
	4-65	RANGOON					15	28,1
		HONGKONG					0	
		PENANG					91	876,39
		JESSELTON					0	
		SINGAPORE					0	
	SUB-TOTAL						106	904,5
	TOTAL						502	2,976,8
GRAND TOTAL							2,068	6.762,5

DECLASSIFIED E.O. 12065 SECTION 3 (E), NARS DATE

COMPLETION OF PACKAGES BY DESTINATIONS

NO. 5

DATE 8th. oct.

COMPLETED		TOTAL PACKAGES COMPLETED TO DATE				REMARKS
GROSS VOL.	MEAS. TON	NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	
		748	1.518,556	4,301.8	3.794,250	
		49	112,754	219.6	193,672	
		797	1.631,310	4,521.4	3.987,922	
		14	16,392	38.9	34,320	
		59	24,587	15.6	18,735	
		73	40,979	54.5	48,055	
		108	230,103	618.1	545,211	
		181	271,082	672.6	593,266	
		560	1.844,690	3,673.8	3.236,333	
		0	0	0	0	
		560	1.844,690	3,673.8	3.236,333	
		27	38,001	83.7	73,812	
		1	630	1.4	1,234	
		28	38,631	85.1	75,046	
		588	1.883,321	3,758.9	3.311,379	
		150	345,666	1,116.5	984,719	
		28	87,850	204.2	180,094	
		187	1.489,558	1,791.4	1.579,973	
		6	31,780	173.0	152,585	
		25	117,444	419.2	369,737	
		396	2.072,298	3,704.3	3.267,108	
		15	28,140	47.2	41,624	
		0	0	0	0	
		91	876,390	1099.1	969,371	
		0	0	0	0	
		0	0	0	0	
		106	904,530	1,146.3	1.010,995	
		502	2,976,828	4,850.6	4278,103	
		2,068	6.762,541	13.803.5	12.170,670	

DECLASSIFIED E.O. 12356 Section 3.3

DAILY REPORT ON COMPLETION OF PACKA

RECIPIENT NATION	ALLOCATION NO.	DESTINATION	PACKAGES COMPLETED NO. OF PACKAGE	GROSS WT.	GROSS VOL. MEAS. TON	TOTAL NO. OF PACKAGE	TOTAL GRO
CHINA	1-68	KEELUNG				748	1.
	1-69	"				49	
	TOTAL					797	1.
NETHER-LAND	2-60	SOURABAYA				14	
		BATAVIA				59	
	SUB-TOTAL					73	
	2-61	BATAVIA				108	
	TOTAL					181	
PHILIPPINE	3-60	MANILA				560	1.
		MANILA SHIPYARD				0	
	SUB-TOTAL					560	1.
	3-61	MANILA				27	
		MANILA SHIPYARD				1	
	SUB-TOTAL					28	
	TOTAL					588	1.
UNITED KINGDOOM	4-63	RANGOON				150	
		HONG KONG				28	
		PENANG				187	1
		JESSELTON				6	
		SINGAPORE				25	
	SUB-TOTAL					396	2
	4-65	RANGOON				15	
		HONG KONG				0	
		PENANG				91	
		JESSELTON				0	
		SINGAPORE				0	
	SUB-TOTAL					106	
	TOTAL					502	2
GRAND TOTAL						2,068	6

COMPLETION OF PACKAGES BY DESTINATIONS

NO. 6

DATE 9th. Oct.

AGES COMPLETED		TOTAL PACKAGES COMPLETED TO DATE				
WT.	GROSS VOL. MEAS. TON	NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	REMARKS
		748	1.518,556	4,301.8	3.794,250	
		49	112,754	218.6	193,672	
		297	1.631,310	4,521.4	3.987,922	
		14	16,392	38.9	34,320	
		59	24,587	15.6	13,735	
		73	40,979	54.5	48,055	
		108	230,103	618.1	545,211	
		181	271,082	672.6	593,266	
		560	1.844,690	3,673.8	3.236,333	
		0	0	0	0	
		560	1,844,690	3,673.8	3.236,333	
		27	38,001	83,7	73,812	
		1	630	1.4	1,234	
		28	38,631	85.1	75,046	
		588	1.883,321	3,758.9	3.311,379	
		150	345,666	1.116.5	984,719	
		28	87,850	204.2	180,094	
		187	1.489,558	1.791.4	1.579,973	
		6	31,780	173.0	152,585	
		25	117,444	419.2	369,737	
		396	2072,298	3.704.3	3.267,108	
		15	28,140	47.2	44,624	
		0	0	0	0	
		91	876,390	1,099.1	969,371	
		0	0	0	0	
		0	0	0	0	
		106	904,530	1,146.3	1.010,995	
		502	2.976,828	4.850.6	4.278,103	
		2,068	6.762,541	13,803.5	12.170,670	

DAILY REPORT ON COMPLETION OF PACK

RECIPIENT NATION	ALLOCATION NO.	DESTINATION	PACKAGES COMPLETED				TO	
			NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON.	NO. OF PACKAGE	G
CHINA	1-68	KEELUNG	0	0	0	0	748	
	1-69	"	78	128,345	211.8	186,776	127	
	TOTAL		78	128,345	211.8	186,776	875	
NETHER-LAND	2-60	SOURABAYA					14	
		BATAVIA					59	
	SUB-TOTAL						73	
	2-61	BATAVIA					108	
	TOTAL						181	
PHILIPPINE	3-60	MANILA					560	
		MANILA SHIPYARD					0	
	SUB-TOTAL						560	
	3-61	MANILA					27	
		MANILA SHIPYARD					1	
	SUB-TOTAL						28	
	TOTAL						588	
UNITED KINGDOOM	4-63	RANGOON					150	
		HONG KONG					28	
		PENANG					187	
		JESSELTON					6	
		SINGAPORE					25	
	SUB-TOTAL						396	
	4-65	RANGOON	1	150	0.3	0.264	16	
		HONGKONG	0	0	0	0	0	
		PENANG	25	241,130	228.5	201,529	116	
		JESSELTON	0	0	0	0	0	
		SINGAPORE	0	0	0	0	0	
	SUB-TOTAL		26	241,280	228.8	201,793	132	
	TOTAL		26	241,280	228.8	201,793	528	
GRAND TOTAL			104	369,625	440.6	388,569	2,172	

COMPLETION OF PACKAGES BY DESTINATIONS

NO. 7

DATE 10th. Oct.

GES COMPLETED			TOTAL PACKAGES COMPLETED TO DATE				REMARKS
WT.	GROSS VOL.	MEAS. TON	NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	
0	0	0	748	1,518,556	4,301.8	3.724,250	
45	211.8	186,776	127	241,099	431.4	380,448	
45	211.8	186,776	875	1.759,655	4,733.2	4.174,698	
			14	16,392	38.9	34,320	
			59	24,587	15.6	13,735	
			73	40,979	54.5	48,055	
			108	238,103	618.1	545,211	
			181	271,082	672.6	593,266	
			560	1,844,690	3,673.8	3.236,333	
			0	0	0	0	
			560	1.844,690	3,673.8	3236,333	
			27	38,001	83.7	73,812	
			1	630	1.4	1,234	
			28	38,631	85.1	75,046	
			588	1.883,321	3,758.9	3.311,379	
			150	345,666	1,116.5	984,719	
			28	87,850	204.2	180,094	
			187	1.489,558	4,791.4	1.579,973	
			6	31,780	173.0	152,585	
			25	117,444	419.2	369,737	
			396	2.072,298	3,704.3	3267,108	
0	0,3	0,264	16	28,290	47.5	41,888	
0	0	0	0	0	0	0	
30	228.5	201,529	116	1.117,520	1.327.6	1.170,900	
0	0	0	0	0	0	0	
0	0	0	0	0	0	0	
30	228.8	201,793	132	1.145,810	1,375.1	1.212,788	
30	228.8	201,793	528	3.218,108	5,079.4	4.429,896	
75	440.6	383,569	2.172	7.132,166	14,244.1	12.559,239	

DAILY REPORT ON COMPLETION OF PACKAGE

RECIPIENT NATION	ALLOCATION NO.	DESTINATION	PACKAGES COMPLETED NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	TOTAL NO. OF PACKAGE	TOTAL GROSS
CHINA	1-68	KEELUNG	18	33,320	127.4	112,361	766	1.551
	1-69	"	25	122,293	189.7	167,305	152	363
	TOTAL		43	155,613	317.1	279,666	918	1.915
NETHER-LAND	2-60	SOURABAYA					14	16
		BATAVIA					59	24
	SUB - TOTAL						73	40
	2-61	BATAVIA					108	230
	TOTAL						181	271
PHILIPPINE	3-60	MANILA					460	1.844
		MANILA SHIPYARD					0	
	SUB - TOTAL						460	1.844
	3-61	MANILA					27	38
		MANILA SHIPYARD					1	
	SUB - TOTAL						28	38
	TOTAL						488	1.883
UNITED KINGDOOM	4-63	RANGOON					150	345
		HONG KONG					28	87
		PENANG					187	1.489
		JESSELTON					4	31
		SINGAPORE					25	117
	SUB - TOTAL						396	2.072
	4-65	RANGOON					16	28
		HONG KONG					0	
		PENANG					116	1.117
		JESSELTON					0	
		SINGAPORE					0	
	SUB - TOTAL						132	1.145
	TOTAL						528	3.218
GRAND TOTAL			43	155,613	317.1	279,666	2.215	7.287

COMPLETION OF PACKAGES BY DESTINATIONS

NO. 8

DATE 11th. Oct.

GES COMPLETED			TOTAL PACKAGES COMPLETED TO DATE				REMARKS
WT.	GROSS VOL.	MEAS. TON.	NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	
320	127.4	112,361	766	1.551,876	4.429.2	3.906,611	
293	189.7	167,305	152	363,392	621.1	547,253	
413	317.1	279,666	918	1.915,268	5,050.3	4454,364	
			14	16,392	38.9	34,320	
			59	24,587	15.6	13,735	
			73	40,979	54.5	48,055	
			108	230,103	618.1	545,211	
			181	271,082	672.6	593,266	
			460	1.844,690	3,673.8	3236,333	
			0	0	0	0	
			460	1.844,690	3,673.8	3.236,333	
			27	38,001	83.7	73,812	
			1	630	1.4	1,234	
			28	38,631	85.1	75,046	
			588	1.883,321	3,758.9	3.311,379	
			150	345,666	1,116.5	984,219	
			28	87,850	204.2	180,094	
			187	1.489,558	1,791.4	1.579,973	
			4	31,780	173.0	152,585	
			25	117,444	419.2	369,737	
			396	2.072,298	3,704.3	3.267,108	
			16	28,290	47.5	41,888	
			0	0	0	0	
			116	1.117,520	1,327.6	1.170,900	
			0	0	0	0	
			0	0	0	0	
			132	1.144,810	1,375.1	1.212,788	
			528	3.218,108	5,079.4	4.479,896	
413	317.1	279,666	2.215	7.287,779	14,561.2	12.838,905	

DAILY REPORT ON COMPLETION OF PACKAGE

RECIPIENT NATION	ALLOCATION NO.	DESTINATION	PACKAGES COMPLETED NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	TOTAL NO. OF PACKAGE	TOTAL GROSS
CHINA	1-68	KEELUNG					766	1.54
	1-69	"					152	36
	TOTAL						918	1.91
NETHER-LAND	2-60	SOURABAYA					14	1
		BATAVIA					59	2
	SUB-TOTAL						73	4
	2-61	BATAVIA					108	23
	TOTAL						181	27
PHILIPPINE	3-60	MANILA					560	1.84
		MANILA SHIPYARD					0	
	SUB-TOTAL						560	1.84
	3-61	MANILA					27	3
		MANILA SHIPYARD					1	
	SUB-TOTAL						28	3
	TOTAL						588	1.88
UNITED KINGROOM	4-63	RANGOON					150	34
		HONG KONG					28	8
		PENANG					187	1.48
		JESSELTON					6	3
		SINGAPORE					25	11
	SUB-TOTAL						396	2.07
	4-65	RANGOON					16	2
		HONG KONG					0	
		PENANG					116	1.11
		JESSELTON					0	
		SINGAPORE					0	
	SUB-TOTAL						132	1.145
	TOTAL						528	3.218
GRAND TOTAL							2215	7.287

N COMPLETION OF PACKAGES BY DESTINATIONS

NO. 9

DATE 12th. Oct.

KAGES COMPLETED			TOTAL PACKAGES COMPLETED TO DATE				
SS WT.	GROSS VOL.	MEAS. TON	NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	REMARKS
			766	1.551,876	4429.2	3.906,611	
			152	363,392	621.1	547,753	
			918	1.915,268	5,050.3	4.454,364	
			14	16,392	38.9	34,320	
			59	24,587	15.6	13,735	
			73	40,979	54.5	48,055	
			108	230,103	618.1	545,211	
			181	271,082	672.6	593,266	
			560	1.844,690	3,673.8	3.236,333	
			0	0	0	0	
			560	1.844,690	3,673.8	3.236.333	
			27	38,001	83.7	73,812	
			1	630	1.4	1,234	
			28	38,631	85.1	75,046	
			588	1.883,381	3,758.9	3.311,379	
			150	345,666	1,116.5	984,219	
			28	87,850	204.2	180,094	
			187	1.489,558	1.791.4	1.579,973	
			6	31,780	173.0	152,585	
			25	117,444	419.2	369,737	
			396	2.072,298	3,704.3	3.267,108	
			16	28,290	47.5	41,888	
			0	0	0	0	
			116	1.117,520	1,327.6	1.170,900	
			0	0	0	0	
			0	0	0	0	
			132	1.145,810	1,375.1	1.212,788	
			528	3.218,108	5,079.4	4.479,896	
			2,215	7.287,779	14,561.2	12.838,905	

DAILY REPORT ON COMPLETION OF PACKA

RECIPIENT NATION	ALLOCATION NO.	DESTINATION	PACKAGES COMPLETED				TOTA	
			No. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	NO. OF PACKAGE	GRO
CHINA	1-68	KEELUNG					766	1.
	1-69	"					152	
	TOTAL						918	1.
NETHER-LAND	2-60	SOURABAYA					14	
		BATAVIA					59	
	SUB - TOTAL						73	
	2-61	BATAVIA					108	
	TOTAL						181	
PHILIPPINE	3-60	MANILA	115	284,280	959.6	846,332	575	2
		MANILA SHIPYARD					0	
	SUB - TOTAL		115	284,280	959.6	846,332	575	2
	3-61	MANILA					27	
		MANILA SHIPYARD					1	
	SUB - TOTAL						28	
	TOTAL		115	284,280	959.6	846,332	703	2
UNITED KINGDOOM	4-63	RANGOON	7	29,800	80.6	71,086	157	
		HONG KONG					28	
		PENANG	21	49,740	104.4	92174	208	1
		JESSELTON					6	
		SINGAPORE					25	
	SUB - TOTAL		28	79,540	185.0	163,160	424	2
	4-65	RANGOON					16	
		HONG KONG					0	
		PENANG					116	1.
		JESSELTON					0	
		SINGAPORE					0	
	SUB - TOTAL						132	1.
	TOTAL		28	79,540	185.0	163,160	556	3.
GRAND TOTAL			143	363,820	1,144.6	1.009,492	2,358	7.

COMPLETION OF PACKAGES BY DESTINATIONS

NO. 10

DATE 13th. Oct.

ES COMPLETED			TOTAL PACKAGES COMPLETED TO DATE				REMARKS
WT.	GROSS VOL.	MEAS. TON.	NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON.	
			366	1.551,876	4,429.2	3.906.611	
			152	363,392	621.1	547,753	
			918	1.915,268	5,050.3	4.454,364	
			14	16,392	38.9	34,320	
			59	24,687	15.6	13,735	
			73	40,979	54.5	48,055	
			108	230,103	618.1	545,211	
			181	271,082	672.6	593,266	
80	959.6	846,332	575	2.128,690	4,633.4	4.082,665	
			0	0	0	0	
80	959.6	846,332	575	2.128,690	4,633.4	4,082,665	
			27	38,001	83.7	73,812	
			1	630	1.4	1,234	
			28	38,631	85.1	75,046	
80	959.6	846,332	703	2.167,201	4,718.5	4,157,711	
00	80.6	71,086	157	375,466	1,197.1	1.055,805	
			28	87,850	204.2	180,094	
40	104.4	92174	208	1.539,298	1,895.8	1.672,047	
			6	31,780	173.0	152,585	
			25	117,444	419.2	369,737	
40	185.0	163,160	424	2.151,838	3,889.3	3.430,268	
			16	28,290	47.5	41,888	
			0	0	0	0	
			116	1.117,520	1,327.6	1.170,900	
			0	0	0	0	
			0	0	0	0	
			132	1.145,810	1,375.1	1.212,788	
20	185.0	163,160	556	3.297,648	5,264.4	4.643,056	
20	1,144.6	1.009,492	2,358	7.651,199	15,705.8	13.848,397	

DAILY REPORT ON COMPLETION OF PACKAG

RECIPIENT NATION	ALLOCATION NO.	DESTINATION	PACKAGES COMPLETED				TOTAL	
			NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	NO. OF PACKAGE	GROSS
	1-68	KEELUNG					766	1.5
CHINA	1-69	"	32	58,720	114.0	100,534	184	4
	TOTAL		32	58,720	114.0	100,534	950	1.9
	2-60	SOURABAYA					14	
		BATAVIA					59	
NETHER	SUB - TOTAL						73	
-LAND	2-61	BATAVIA					108	2
	TOTAL						181	2
	3-60	MANILA	19	92,230	219.3	193,414	594	2.2
		MANILA SHIPYARD					0	
	SUB - TOTAL						594	2.2
PHILIPPINE	3-61	MANILA					27	
		MANILA SHIPYARD					1	
	SUB - TOTAL						28	
	TOTAL		19	92,230	219.3	193,414	522	2.2
	4-63	RANGOON	12	36,300	111.8	98,603	169	4
		HONG KONG					28	
		PENANG	32	54,520	113.2	99,831	240	1.5
		JESSELTON					6	
		SINGAPORE					25	1
UNITED KINGDOOM	SUB - TOTAL						468	22
	4-65	RANGOON					16	
		HONG KONG					0	
		PENANG	6	83,560	92.5	81,581	122	1.2
		JESSELTON					0	
		SINGAPORE					0	
	SUB - TOTAL						138	1.2
	TOTAL		50	174,380	317.5	280,015	606	3.4
GRAND TOTAL			101	325,330	650.8	573,963	2.459	7.5

ON COMPLETION OF PACKAGES BY DESTINATIONS

NO. 11

DATE 4th Oct.

AGES COMPLETED			TOTAL PACKAGES COMPLETED TO DATE				
S WT.	GROSS VOL.	MEAS. TON	NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	REMARKS
			766	1.551,876	4429.2	3,906,611	
8,720	114.0	100,534	184	422,165	735.2	648,375	
8,720	114.0	100,534	950	1.974,041	5,164.4	4,554,986	
			14	16,392	38.9	34,320	
			59	24,587	15.6	13,735	
			73	40,979	54.5	48,055	
			108	230,103	618.1	545,211	
			181	271,082	672.6	593,266	
230	219.3	193,414	594	2.221,200	4852.7	4276,069	
			0	0	0	0	
			594	2.221,200	4,852.7	4.276,069	
			27	38,001	83.7	73,812	
			1	630	1.4	1,234	
			28	38,631	85.1	75,046	
230	219.3	193,414	522	2.259,831	4937.8	4.351,115	
300	111.8	98,603	169	412,016	1,308.9	1,154,408	
			28	87,850	2042	180,094	
520	113.2	99,831	240	1.593,818	2,009.0	1.771,878	
			6	31,780	173.0	152,585	
			25	117,444	419.2	369,737	
			468	2242,908	4,114.3	3.628,702	
			16	28,290	47.5	41,888	
			0	0	0	0	
560	92.5	81,581	122	1.201,080	1,420.1	1.252,481	
			0	0	0	0	
			0	0	0	0	
			138	1.229,370	1,467.6	1.294,369	
380	317.5	280.015	606	3.472,278	5,581.9	4923,071	
30	650.8	573,963	2.459	7.977,232	16,356.7	14.423,438	

DAILY REPORT ON COMPLETION OF [illegible] KAGES

RECIPIENT NATION	ALLOCATION NO.	DESTINATION	PACKAGES COMPLETED NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	TOTAL PACK NO. OF PACKAGE	TOTAL PACK GROSS WT.
CHINA	1-68	KEELUNG					766	1.551,876
	1-69	"					184	422,165
	TOTAL						950	1.974,041
NETHER-LAND	2-60	SOURABAYA					14	16,392
		BATAVIA					59	24,587
	SUB-TOTAL						73	40,979
	2-61	BATAVIA					108	230,103
	TOTAL						181	271,082
PHILIPPINE	3-60	MANILA					594	2.221,200
		MANILA SHIPYARD					0	0
	SUB-TOTAL						594	2.221,200
	3-61	MANILA					27	38,001
		MANILA SHIPYARD					1	630
	SUB-TOTAL						28	38,631
	TOTAL						722	2.259,831
UNITED KINGDOM	4-65	RANGOON					169	412,016
		HONG KONG					28	87,850
		PENANG					240	1.593,818
		JESSELTON					6	31.780
		SINGAPORE					25	117,444
	SUB-TOTAL						468	2.242,908
	4-65	RANGOON					16	28,290
		HONG KONG					0	0
		PENANG					122	1.201,080
		JESSELTON					0	0
		SINGAPORE					0	0
	SUB-TOTAL						138	1.229,370
	TOTAL						606	3.472,278
GRAND TOTAL							2.459	7.977,232

COMPLETION OF PACKAGES BY DESTINATIONS

NO. 12

DATE 15th. oct.

COMPLETED			TOTAL PACKAGES COMPLETED TO DATE			
GROSS VOL.	MEAS. TON	NO. OF PACKAGE	GROSS WT.	GROSS VOL.	MEAS. TON	REMARKS
		766	1.551,876	4.429.2	3,906,611	
		184	422,165	735.2	648,375	
		950	1.974,041	5,164.4	4,554,986	
		14	16,392	38.9	34.320	
		59	24,587	15.6	13,735	
		73	40,979	54.5	48,055	
		108	230,103	618.1	545,211	
		181	271,082	672.6	593,266	
		594	2.221,200	4,852.7	4.276,069	
		0	0	0	0	
		594	2.221,200	4,852.7	4.276,069	
		27	38,001	83.7	73,812	
		1	630	14	1.234	
		28	38,631	85.1	75,046	
		522	2.259,831	4,937.8	4,351,115	
		169	412,016	1,308.9	1,154,408	
		28	87,850	204.2	180,094	
		240	1.593,818	2,009.0	1,771,878	
		6	31.780	173.0	152,585	
		25	117,444	419.2	369,737	
		468	2.242,908	4,114.3	3,628,702	
		16	28,290	47.5	41,888	
		0	0	0	0	
		122	1.201,080	1,420.1	1.252,481	
		0	0	0	0	
		0	0	0	0	
		138	1.229,370	1,467.6	1,294,369	
		606	3.472,278	5,581.9	4,923,071	
		2.459	7.977,232	16,356.7	14,422,438	

Copy

file
Packaging & Crating
Relocation Notices

TS/a1

KINKI LIAISON & COORDINATION OFFICE

Prefectural Building
OSAKA

KKLCO No. 860 ER

6 October 1949

TO : Chief,
Osaka Civil Affairs Team

SUBJECT: Weekly Packaging Schedule,
Osaka Arsenal (32-32)

For your information.

S. Shima
Director

Incl: Letter from Osaka Finance Division,
OFO No. 49, 4 October 1949, subject
as stated above.

OSAKA FINANCE OFFICE
(Osaka)

4 October 1949

OFO No. 49

TO : Economics Division,
Osaka Civil Affairs Team

THROUGH: Kinki Liaison Office

SUBJECT: Weekly Packaging Schedule, Osaka Arsenal
(32 - 32)

1. This Office humbly submits to your headquarters the attached weekly packaging schedules by allocation notices.

2. These packaging schedules were compiled in compliance with the verbal request of Mr. Laffin of CHQ, SCAP.

FOR THE CHIEF:

Incl: Weekly Schedule

KKLCC
Received: 4 AM PM 5/10/49

M. Matsuda
Vice Chief

KM/ym/ek

WEEKLY PACKAGING SCHEDULE

Allocation Notice: ~~1 - 69~~

Week	Destination	No. of Mach.	No. of Packages	Cubage (Cub. M)	Gross Weight	Measurment
1st (Oct.1)	Keelung	51	59	312.2	86,250	280,801
2nd (Oct.2 thru Oct.8)	"	97	239	1850.2	385,500	1633,464
3rd (Oct.9 thru Oct.15)	"	11	129	127.3	207.640	112,279
4th (Oct.16 thru Oct.22)	"	14	116	133.8	196,250	118.012
5th (Oct.23 thru Oct.29)	"	9	112	619.2	408.260	546,134
Sub-Total		182	655	3043.2	1883,900	2690,690 ~~2664,102~~
* Unknown Week	"	33	634	4366.9	2633.485	3869.250
Total		215	1289	7430.1	3917.385 ~~3875,802~~	6559.940 ~~6539,305~~

* 31 Overhead Travelling Cranes
1 Trackage
1 Transformer

WEEKLY PACKAGING SCHEDULE

Allocation Notice No.: 1-69

Week	Destination	No.of Mach.	No.of Package	Cubage (Cub.M.)	Gross Weight	Measurment
1st (Oct 1)	Keelung	154	116	416.4	241,780	357,267
2nd (Oct 2 thru Oct 8)	"	282	415	1,178.8	777,052	1,039,702
3 rd (Oct 9 thru Oct 15)	"	145	217	896.4	566,678	790,625
4th (Oct 16 thru Oct 22)	"	24	78	184.3	184.836	162,553
5th (Oct 23 thru Oct 29)	"	5	30	44.8	65,420	39,514
Sub-Total:		610	856	2,720.7	1,835,766	2,399,661
x Unknown Week	Keelung	35	53	269.3	74,418	237,523
Total:		645	909	2,990.0	1,910,184	2,637,184

x Equipment for Substation:

24 Transformers
6 Switch Gear Panels
2 Switch Box
1 Panel Marble
1 Control Panel
1 Overhead Travelling Crane.

WEEKLY PACKING SCHEDULE

Allocation Notice No.: 2-60

Week	Destination	No.of Mach.	No.of Package	Cubage (Cub.M.)	Gross Weight	Measur-ment
2nd (Oct 2 thru Oct 8)	Batavia	2	2	2.8	6,400	2,470
Total:		2	2	2.8	6,400	2,470

WEEKLY PACKING SCHEDULE

Allocation Notice No.: 2-61

Week	Destination	No.of Mach.	No.of Package	Cubage (Cub.M.)	Gross Weight	Measurment
1st (Oct 1)	Batavia	2	2	9.7	4,160	8,555
4th (Oct 15 thru Oct 22)	"	1	13	14.1	21,540	12,436
Sub-Total		3	15	23.8	25,700	21,991 ~~21,091~~
x Unknown Week	Batavia	2	47	190.0	475,000	167,580
Total:		5	62	213.8	500,700	189,571 ~~189,671~~

x 1 Overhead Travelling Crane
1 Motor

WEEKLY PACKING SCHEDULE

Allocation Notice No.: 3-60

Week	Destination	No.of Mach.	No. of Package	Cubage (Cub.M)	Gross Weight	Measurment
1st (Oct 1)	Manila	14	21	34.5	56,180	30,429
2nd (Oct 2 thru Oct 8)	"	9	149	378.9	172,130	334.190
3rd (Oct 9 thru Oct 15)	"	13	34	211.7	204,880	186,719
4th (Oct 16 thru Oct 22)	"	12	40	179.0	125,000	157,878
5th (Oct 22 thru Oct 39)	"	9	79	183.1	197,050	171,994
Sub-Total		57	323	987.2	755,240	881,210
*Unknown Week	"	6	76	627.1	312,180	553,102
Total		63	399	1,614.3	1,067,420	1,434,312

* 5 Overhead Travelling Cranes
1 Switch Gear Panel

WEEKLY PACKAGING SCHEDULE

Allocation Notice No.: 3-61

Week	Destination	No. of Mach.	No. of Package	Cubage (Cub. M)	Gross Weight	Measurment
2nd (Oct 2 thru Oct 8)	Manila	120	74	210.5	263,696	189,621
3rd (Oct 9 thru Oct 15)	"	2	25	182.5	189,550	160,965
4th (Oct 16 thru Oct 22)	"	6	7	15.0	12,000	13,230
Total		128	106	408.0	465,246	363,816

WEEKLY PACKAGING SCHEDULE

Allocation Notice No. 4-63

Week	Allocation No.	Destination	No. of Machine	No. of Package	Cubage (Cub. m.)	Gross Weight (kg)	Measurement
1st (Oct. 1)	4-63	Penang	1	18	170.9	160,130	150.734
Total:			1	18	170.9	160.130	150.734
4th (Oct. 16 thru Oct. 22)	4-63	Rangoon	2	17	176.2	36,000	155.408
Sub Total:			2	17	176.2	36,000	155.408
# Unknown Week	"	"	4	20	28.0	38,750	24.696
Total:			6	37	204.2	74.750	180.104
# Unknown Week	4-63	Jesselton	1	3	9.5	10,000	8.379
Total:			1	3	9.5	10,000	8.379

Overhead Travelling Cranes.

WEEKLY PACKING SCHEDULE

Allocation Notice No.: 4-65

Week	Destination	No.of Mach.	No. of Package	Cubage (Cub.M.)	Gross Weight	Measurment
2nd (Oct 2 thru Oct 8)	Hongkong	1	12	226.3	164,480	199,597
4th (Oct 16 thru Oct 22)	"	2	89	580.0	290,000	511,560
Total:		3	101	806.3	454,480	711,157
3rd (Oct 9 thru Oct 15)	Singapore	3	15	48.4	64,380	42,689
4th (Oct 16 thru Oct 22)	"	2	20	55.6	73,960	49,039
Total:		5	35	104.0	138,340	91,728
2nd (Oct 2 thru Oct 8)	Jesselton	1	2	1.9	1,700	16,758
Total:		1	2	1.9	1,700	16,758
1st (Oct 1)	Penang	19	97	518.7	550,680	457,493
2nd (Oct 2 thru Oct 8)	"	46	213	2,195.2	1,567,960	1,936,166
3rd (Oct 9 thru Oct 15)	"	19	190	1,613.8	1,050,630	1,423,772
4th (Oct 16 thru Oct 22)	"	4	26	64.5	80,500	56,889
5th (Oct 23 thru Oct 29)	"	2	38	320.0	110,000	28,224
Total:		90	564	4,712.2	3,359,770	3,902,544

Allocation Notice No.: 4-65 (cont'd)

Week	Destination	No.of Mach.	No. of Package	Cubage (Cub.M)	Gross Weight	Measurment
1st (Oct 1)	Rangoon	65	65	67.9	47,880	59,988
2nd (Oct 2 thru Oct 8)	"	31	27	50.1	55,500	44,188
3rd (Oct 9 thru Oct 15)	"	20	29	8.4	10,420	7,309
4th (Oct 16 thru Oct 22)	"	40	41	156.0	89,960	137,592
5th (Oct 22 thru Oct 29)	"	1	9	425.4	27,200	370,916
x Unknown Week	"	15	12	41.8	9,540	36,858
Total:		172	183	~~796.4~~ 749.6	240,500	656,851

x Equipment for Substation: 6 Transformers
8 Switch Gear Panels
1 Switch Box

packaging & crating
allocation Notices

RAS/lmp

HEADQUARTERS
OSAKA CIVIL AFFAIRS TEAM
APO 25

14 October 1949

SUBJECT: Transmittal of Progress Reports and Packing Lists

TO: General Headquarters
Supreme Commander for the Allied Powers
APO 500
ATTN: Civil Property Custodian

1. Herewith transmitted are progress reports regarding Allocation Notices 1-68, 1-69, 2-61, 3-60, 3-61, 4-63 and 4-65, and packing slips for the 331 packages indicated in the reports as having been completed in the reported period.

2. The inclosed report pertains to operations of 7 October only. Most recent progress report previously submitted is for the period 22 September thru 6 October. Effective with the inclosed report, progress reports regarding Osaka Arsenal operations will be transmitted as frequently as can be prepared, instead of the regular bi-weekly period, in compliance with request from Major Vick, Field Operations Division, your headquarters.

3. The progress reports and packing lists, prepared by the Osaka Finance Division, have been reviewed by this headquarters and found to be accurately reflective of the status of operations.

FOR THE CHIEF:

FRED N. ALEXANDER
WOJG USA
Asst Adjutant

13 Incls:
1 thru 7: progress reports (ea dup) for AN's 1-68,1-69, 2-61,3-60,3-61,4-63 & 4-65, in order
8 thru 13: packing lists (ea trip) for AN's 1-68,1-69, 3-60,3-61,4-63 & 4-65, in order

OSAKA M.G
RES-COM-IND
FILE 0-2647

Packaging & Crating
Allocation Notices

GENERAL HEADQUARTERS
SUPREME COMMANDER FOR THE ALLIED POWERS

28 September 1949

AG 387.6 (22 Jul 47)CPC/RP
SCAPIN 5825-A/42

MEMORANDUM FOR: JAPANESE GOVERNMENT

SUBJECT: Amendments to Allocation Notices

1. Reference is made to:

a. Memorandum for the Japanese Government, file AG 387.6 (22 Jul 47)CPC/RP, SCAPIN 5825-A/36, 20 June 1949, subject, "Transmittal of Reparations Allocation Notices," from General Headquarters, Supreme Commander for the Allied Powers.

b. Memorandum for the Japanese Government, file AG 387.6 (22 Jul 47)CPC/RP, SCAPIN 5825-A/40, 30 June 1949, subject, "Transmittal of Reparations Allocation Notices," from General Headquarters, Supreme Commander for the Allied Powers.

2. Inclosures to reference memoranda are amended by the following deletions:

Allocation Notice Number	Page Number	Inventory Number
1-63	7	120
2-60	1	380
	2	1780
2-61	3	D- 471
3-60	7	3765
	13	6067
	13	6068
	14	6195
3-61	1	926
	3	93(1950)
	4	1516
	6	8523
	8	8526
4-63	7	6172
	7	6181

3. Inclosures to reference memoranda are amended by the following corrections:

AG 387.6 (22 Jul 47)CPC/RP
SCAPIN 5025-A/48

Allocation Notice Number	Page Number	Inventory Number	Item Corrected	Corrected to Read
1-68	3	P-71) P-72)	Description	2 Transformers
	4	1423) 1424)	Description	Motor, 20 HP
	4	2890	Description	Vertical Boring & Turning Mill
	5	4949	Description	Startin Compensator
	5	5451) 5452)	Description	Motor, 25 HP
	13	953	Inventory No.	933
	14	958-1 (Oil Tank)	Inventory No.	9589
1-69	10	6361	Description	Winch, 2 T w/o motor
	13	Bldg No. 201	Description	62 Oxygen Tubes
	4	5623	Inventory No.	5652
	8	D-401	Inventory No.	D-400
	8	1437	Description & Additional Inventory No.	Rheostat w/motor 1433 Motor, DC 15 HP, 200 kgs
	13	(1)-109	Inventory No.	(P)-109
	14	14-173	Inventory No.	14-173(7051)
	17	2978	Inventory No.	2998
	21	1711	Inventory No.	1674
	21	1712	Inventory No.	1675
2-60	1	5104	Inventory No.	5184
	1	6045	Inventory No.	6845
	1	6048	Inventory No.	6848
	1	-159	Inventory No. & Description	D-159, Motor AC 30 HP
3-60	1	D-192	Description	Gear Shearing Machine
	7	3788	Description	Horizontal Borer
	17	(1)5415	Description	Steam Hammer
	17	(3)5415	Description	Air Hammer
	19	92	Description	Motor Generator
	11	3009	Addition to Inventory No.as accesories	Inventory Nos. 8523 & 8526
	20	18(1360)	Addition	A motor,30 HP, Inventory No.1360, Wt. 500 kgs
	23	31(5634)	Inventory No.	31(5630)
	15	957-1	Weight	6,700
3-61	3	(58)	Description	Barkers Water Mill (1)
	6	6769	Inventory No.	6796
	8	96794	Inventory No.	957-4

AG 307.6 (22 Jul 47)CPC/RP
GCAPIN 5325-A/43

Allocation Notice Number	Page Number	Inventory Number	Item Corrected	Corrected to Read
4-63	4	P-64	Decription	Mechanical Press w/2 HP Motor
	7	6128	Inventory No.	6129
	8	6198	Inventory No.	6178
	11	70(6429)	Inventory No.	70(6424)
	11	71(6435)	Inventory No.	71(6425)
4-65	2	6732	Inventory No.	6733
	8	32-32 14/203	Inventory No.	7052
	10	32-32(58)	Description	Barkers Mills Models (2)

4. Packing slips prepared for items covered on allocation notices applicable to Osaka Military Arsenal should show inventory numbers and other identification of items allocated as shown on allocation notices as amended. Supplementary inventory numbers, assigned by the custodian subsequently to original inventory and evaluation on which allocation notices are based, if painted on packages or machines, should also be shown on the packing slips as an alternative means of identification. Building number and description of items shiuld be shown in lieu of inventory numbers where the latter do not exist.

5. This is a partial list of amendments. Additional amendments will follow. Revised weight totals will be furnished with final corrections.

FOR THE SUPREME COMMANDER:

R. M. LEVY
Colonel, AGD
Adjutant General

DECLASSIFIED Per NARA Records Disposition Authority

Packaging & Crating
Allocation Notices

HEADQUARTERS
OSAKA CIVIL AFFAIRS TEAM
APO 25

RAS/lmp

13 October 1949

SUBJECT: Transmittal of Progress Reports and Packing Lists

TO: General Headquarters
Supreme Commander for the Allied Powers
APO 500
ATTN: Civil Property Custodian

1. Herewith transmitted are reports of progress, for the period 22 September thru 6 October, in the packaging and crating of Allocation Notices 1-68, 1-69, 2-60, 2-61, 3-60, 3-61, 4-63 and 4-65, at the Osaka Arsenal, plant 32-32.

2. Also inclosed are packing lists for 860 of the 1159 packages cited in the inclosed progress reports as having been completed in the reported period. The remaining 299 packing slips, representing 299 of the 351 packages reported herewith for Allocation Notice 1-68 (Incl No. 1), were previously transmitted under cover of letter, this headquarters, subject: "Transmittal of Packing Slips", 26 September 1949, package numbers as follows: 63 thru 66, 145, 204 thru 207, 217 thru 221, 225 thru 335, 337 thru 360, 362 thru 430, 432, 433, 435 thru 437, 440 thru 513, 516 and 517.

3. The progress reports and packing slips, prepared by the Osaka Finance Office, have been reviewed by this headquarters and found to be accurately reflective of the status of operations.

FOR THE CHIEF:

16 Incls: (ea dup)
1 thru 8: progress reports for AN's 1-68,1-69,2-60, 2-61,3-60,3-61,4-63 & 4-65, in order
9 thru 16: Packing lists for cited progress reports, in same order

FRED N. ALEXANDER
WOJG USA
Asst Adjutant

OSAKA M.G
RES-COM-IND
FILE 0-2695

file
packaging & Crating
Allocation Notices

HEADQUARTERS
OSAKA CIVIL AFFAIRS TEAM
APO 25

HCK/ras/lmp

26 September 1949

SUBJECT: Transmittal of Packing Lists - Allocation Notices 1-68, 3-60 and 4-63

TO: General Headquarters
Supreme Commander for the Allied Powers
APO 500
ATTN: Civil Property Custodian

1. herewith transmitted are packing lists regarding equipment crated in compliance with Allocation Notices 1-68, 3-60 and 4-63 at the Osaka Arsenal, Plant 32-32.

2. The packing lists, prepared by the Osaka Finance Division, have been reviewed by this headquarters and found to be correct.

3. Forwarded in complicance with 8j(2), Operational Directive 21 for 1948.

FOR THE CHIEF:

3 Incls:
Packing lists - Allocation
Notices 1-68,3-60 & 4-63
(ea trip)

FRED N. ALEXANDER
WOJG USA
Asst Adjutant

file
Packaging & Crating
Allocation Notice

HEADQUARTERS
OSAKA CIVIL AFFAIRS TEAM
APO 25

ECK/ras/kk

4 October 1949

SUBJECT: Transmittal of Progress Reports

TO: General Headquarters
Supreme Commander for the Allied Powers
APO 500
ATTN: Civil Property Custodian

1. Herewith transmitted are reports of progress, for the period 16 September thru 22 September, in the packaging and crating of Allocation Notices 1-68, 1-69, 2-60, 3-60, 3-61, 4-63 and 4-65, at the Osaka Arsenal 32-32.

2. The reports, prepared by the Osaka Finance Office, have been reviewed by this headquarters and found to be accurately reflective of the status of operations.

3., Packing lists for the 346 packages cited in the progress reports as having been completed in the reported period were previously transmitted to your headquarters as follows:

a. Packing lists for the 144 packages cited in the report for AN 1-68 (Incl No. 1), were forwarded under cover of letter, this headquarters, subject: "Transmittal of Packing Lists", 22 September 1949. Package numbers as follows: 17, 18, 19, 28, 30, 34, 38, 40, 41, 45, 47, 49, 54, 62, 70, 74, 77, 81, 83, 87, 89, 92 thru 144, 146 thru 157, 171 thru 203, 208 thru 216, 222, 223 and 224.

b. Packing lists for the 10 packages cited in the report for AN 2-60 (Incl No. 3), were delivered to the hand of Mr John Laffin, CPC/Rep, on 17 September 1949. Package numbers as follows: 2 thru 6 and 11 thru 15.

c. Packing lists for the 84 packages cited in the report for AN 2-61 (Incl No. 4); for the 75 packages cited in the report for AN 3-60 (Incl No. 5); and for the 75 packages cited in the report for AN 4-63 (Incl No. 7), were forwarded under cover of letter, this headquarters, subject: "Transmittal of Packing Lists", 26 September 1949. Pertinent package numbers are as follows:

(1) AN 2-61: 1 thru 3, 5, 7, 15, 18, 19, 21, 28 thru 31, 34, 37 thru 54 and 56 thru 107.

Hq Osaka Civil Affairs Team, APO 25 4 Oct 49
Subj: Transmittal of Progress Reports

(2) AN 3-60: 61, 62, 107 thru 137, 139 thru 146, 149 thru 152, 154 thru 159, 162 thru 168, 170 thru 173, 195, 196, 197, 205, 206, 207, 225, 226, 227 and 229 thru 232.

(3) AN 4-63: 32, 47, 49, 53, 83 thru 91, 114 thru 119, 121, 124, 125, 129, 130, 131 and 177 thru 181.

FOR THE CHIEF:

8 Incls:
As above (ea dup)

FRED N ALEXANDER
WOJG USA
Asst Adjutant

OSAKA FINANCE OFFICE
(Osaka)

24 September 1949

OFO No. 40

TO : Economics Division,
Osaka Civil Affairs Team

THROUGH: Kinki Liaison Office

SUBJECT: Progress Report No.3 (Period: Sept. 16 thru 22)

1. This Office respectfully submit the attached Progress Report No.3 pertaining to packaging operation at Osaka Arsenal in accordance with SCAPIN 5825-A/36 and SCAPIN 5825-A/40 dated June 20 and 30, 1949 respectively.

2. The packing lists to be attached to this report has already been submitted to your Headquarters. The submitted packing lists correspond to the following package numbers.

3. Package Numbers:

China (1-68)

Package No.	17,	95,	119,	143,	168,	192,
	18,	96,	120,	144,	169,	193,
	19,	97,	121,	146,	170,	194,
	28,	98,	122,	147,	171,	195,
	30,	99,	123,	148,	172,	196,
	34,	100,	124,	149,	173,	197,
	38,	101,	125,	150,	174,	198,
	40,	102,	126,	151,	175,	199,
	41,	103,	127,	152,	176,	200,
	45,	104,	128,	153,	177,	201,
	47,	105,	129,	154,	178,	202,
	49,	106,	130,	155,	179,	203,
	54,	107,	131,	156,	180,	208,
	62,	108,	132,	157,	181,	209,
	70,	109,	133,	158,	182,	210,
	74,	110,	134,	159,	183,	211,
	77,	111,	135,	160,	184,	212,
	81,	112,	136,	161,	185,	213,
	83,	113,	137,	162,	186,	214,
	87,	114,	138,	163,	187,	215,
	89,	115,	139,	164,	188,	216,
	92,	116,	140,	165,	189,	222,
	93,	117,	141,	166,	190,	223,
	94,	118,	142,	167,	191,	224,

Total: 144

- cont'd -

Nether lands (2-61)

Package No.	1,	30,	45,	57,	68,	78,	88,	98,
	2,	31,	46,	58,	69,	79,	89,	99,
	3,	34,	47,	59,	70,	80,	90,	100,
	5,	37,	48,	60,	71,	81,	91,	101,
	7,	38,	49,	61,	72,	82,	92,	102,
	15,	39,	50,	62,	73,	83,	93,	103,
	18,	40,	51,	63,	74,	84,	94,	104,
	19,	41,	52,	64,	75,	85,	95,	105,
	21,	42,	53,	65,	76,	86,	96,	106,
	28,	43,	54,	66,	77,	87,	97,	107.
	29,	44,	56,	67,				

Total: 84

Netherlands (2-60)

Package No.	2,	3,	4,	5,	6,	11,	12,	13,	14,	15.

Total: 10

Philippines (3-60)

Package No.	61,	116,	127,	139,	152,	166,	205,
	62,	117,	128,	140,	154,	167,	206,
	107,	118,	129,	141,	155,	168,	207,
	108,	119,	130,	142,	156,	170,	225,
	109,	120,	131,	143,	157,	171,	226,
	110,	121,	132,	144,	158,	172,	227,
	111,	122,	133,	145,	159,	173,	229,
	112,	123,	134,	146,	162,	195,	230,
	113,	124,	135,	149,	163,	196,	231,
	114,	125,	136,	150,	164,	197,	232.
	115,	126,	137,	151,	165,		

Total: 75

United Kingdom (4-63)

Package No.	32,	84,	89,	116,	124,	129,	178,
	47,	85,	90,	117,	125,	130,	179,
	49,	86,	91,	118,	126,	131,	180,
	53,	87,	114,	119,	127,	177,	181.
	83,	88,	115,	121,	128,		

Total: 33

FOR THE CHIEF OF OSAKA FINANCE OFFICE:

Incl: Progress Report No.3

pp M. Kambara

MITSUHARU, MATSUDA
Vice Chief,
Osaka Finance Office

KM/sn/kd

PROGRESS REPORT OF INTEGRATED FACILITIES

1. Report No: 3
2. Allocation No: 1 - 68
3. Period Ending: 22 Sept 49

4. Code symbol of plants being reported on: 32 - 32

5. Dismantling, Disassembly, and Packing:

a. Allocation Notice completion date: ____________

b. Present estimates completion date: 25 Oct 49

c. Work completed during report period:

(1) Dismantling and disassembly: 2.3 %

(2) Packing: 5 %

d. Work completed to date:

(1) Dismantling and disassembly: 45.3 %

(2) Packing: 7.5 %

	Number	Gross Weight (metric tons)	Gross Volume (meas. tons)
e. Packages completed during report period:	144	302.468	639.1
f. Packages completed to date:	210	447.13	939.156

6. Remarks: Packaging completion date for crane trackage and sub-station is 28 Nov. 49.

E. Urakami
7. Signature

Chief Custodian
8. Title

9. Reviewed by

10. Signature

11. Title

DECLASSIFIED E.O. 12065 SECTION 3.3(b)(1)

PROGRESS REPORT OF INTEGRATED FACILITIES

1. Report No: 1

2. Allocation No: 1 - 69

3. Period Ending: 22 Sept 49

4. Code symbol of plants being reported on: 32 - 32

5. Dismantling, Disassembly, and Packing:

   a. Allocation Notice completion date: _____

   b. Present estimates completion date: 25 Oct 49

   c. Work completed during report period:

      (1) Dismantling and disassembly: 9.2 %

      (2) Packing: 0

   d. Work completed to date:

      (1) Dismantling and disassembly: 92 %

      (2) Packing: 0

	Number	Gross Weight (metric tons)	Gross Volume (meas. tons)
e. Packages completed during report period:	0	0	0
f. Packages completed to date:	0	0	0

6, Remarks: Packaging operation completion date for transformer and crane is 20 Nov. 1949.

E. Urakami

7. Signature Chief Custodian

8. Title

9. Reviewed by

10. Signature

11. Title

PROGRESS REPORT OF INTEGRATED FACILITIES

1. Report No: 3

2. Allocation No: 2 - 60

3. Period Ending: 22 Sept 49

4. Code symbol of plants being reported on: 32 - 32

5. Dismantling, Disassembly, and Packing:

a. Allocation Notice completion date: ____________

b. Present estimates completion date: 15 Sept 49

c. Work completed during report period:

(1) Dismantling and disassembly: 0

(2) Packing: 5 %

d. Work completed to date:

(1) Dismantling and disassembly: 100 %

(2) Packing: 39.7 %

	Number	Gross Weight (metric tons)	Gross Volume (meas. tons)
e. Packages completed during report period:	10	8.568	17.82
f. Packages completed to date:	15	18.198	38.55

6, Remarks: Inspection ready for 58 packages.

E. Urakami

7. Signature

Chief Custodian

8. Title

9. Reviewed by

10. Signature

11. Title

DECLASSIFIED E.O. 12958, Sec. 3.3

PROGRESS REPORT OF INTEGRATED FACILITIES

1. Report No: 3
2. Allocation No: 2 - 61
3. Period Ending: 22 Sept 49
4. Code symbol of plants being reported on: 32 - 32
5. Dismantling, Disassembly, and Packing:
   a. Allocation Notice completion date:
   b. Present estimates completion date: 25 Oct 49
   c. Work completed during report period:
      (1) Dismantling and disassembly: 2.8 %
      (2) Packing: 64 %
   d. Work completed to date:
      (1) Dismantling and disassembly: 50.8 %
      (2) Packing: 82 %

	Number	Gross Weight (metric tons)	Gross Volume (meas. tons)
e. Packages completed during report period:	84	193.578	461.99
f. Packages completed to date:	107	228.005	531.93

6. Remarks: Packaging completion date for crane and substation is 28 Nov 49.

E. Urakami

7. Signature

Chief Custodian

8. Title

9. Reviewed by

10. Signature

11. Title

DECLASSIFIED E.O. 12958, Sec. 3.5

PROGRESS REPORT OF INTEGRATED FACILITIES

1. Report No: 3
2. Allocation No: 3 - 60
3. Period Ending: 22 Sept 49
4. Code symbol of plants being reported on: 32 - 32
5. Dismantling, Disassembly, and Packing:
   a. Allocation Notice completion date:
   b. Present estimates completion date: 20 Sept 49
   c. Work completed during report period:
      (1) Dismantling and disassembly: 2.3 %
      (2) Packing: 5 %
   d. Work completed to date:
      (1) Dismantling and disassembly: 56 %
      (2) Packing: 5.38 %

	Number	Gross Weight (metric tons)	Gross Volume (meas. tons)
e. Packages completed during report period:	75	151.917	312.76
f. Packages completed to date:	141	294.3845	636.63

6. Remarks: (1) Completion date for crane and surface plate is 28 Nov 49.
   (2) Packaging operation completed on all items other than the above. About 600 items being readied for inspection.
7. Signature: C. Arakami
8. Title: Chief Custodian
9. Reviewed by
10. Signature
11. Title

PROGRESS REPORT OF INTEGRATED FACILITIES

1. Report No: 1

2. Allocation No: 3-61

3. Period Ending: 22 Sep 49

4. Code symbol of plants being reported on: 32-32

5. Dismantling, Disassembly, and Packing:

a. Allocation Notice completion date:

b. Present estimates completion date: 25 Oct 49

c. Work completed during report period:

(1) Dismantling and disassembly: 10.5 %

(2) Packing: 0

d. Work completed to date:

(1) Dismantling and disassembly: 10.5 %

(2) Packing: 0

	Number	Gross Weight (metric tons)	Gross Volume (meas. tons)
e. Packages completed during report period:	0	0	0
f. Packages completed to date:	0	0	0

6, Remarks:

7. Signature E. Urakami

Chief Custodian

8. Title

9. Reviewed by

10. Signature

11. Title

PROGRESS REPORT OF INTEGRATED FACILITIES

1. Report No: 3
2. Allocation No: 4-63
3. Period Ending: 22 Sep 49
4. Code symbol of Plants being reported on: 32-32
5. Dismantling, Disassembly, and Packing:
   a. Allocation Notice completion date: _____
   b. Present estimates completion date: 20 Sep 49
   c. Work completed during report period
      (1) Dismantling and disassembly: 1.1 %
      (2 Packing: 5 %
   d. Work completed to date:
      (1) Dismantling and disassembly: 67.75%
      (2) Packing: 18.01%

	Number	Gross Weight (metric tons)	Gross Volume (meas. tons)
e. Packages completed during report period:	33	104.28	78.85
f. Packages completed to date:	104	250.523	377.142

6. Remarks:

   1. Packaging completion date for crane, surface plate and sub-station is 28 Nov. 1949.

   2. Packaging operation completed on all items other than the above. About 300 items being readied for inspection.

E. Urakami
Signature
Chief Custodian
8. Title

9. Reviewed by:

10. Signature

11. Title

PROGRESS REPORT OF INTEGRATED FACILITIES

1. Report No: 1
2. Allocation No: 4-65
3. Period Ending: 22 Sep 49
4. Code symbol of Plants being reported on: 32-32
5. Dismantling, Disassembly, and Packing:
   a. Allocation Notice completion date:
   b. Present estimates completion date: 25 Oct 49
   c. Work completed during report period
      (1) Dismantling and disassembly: 12.9 %
      (2 Packing: 0
   d. Work completed to date:
      (1) Dismantling and disassembly: 12.9 %
      (2) Packing: 0

	Number	Gross Weight (metric tons)	Gross Volume (meas. tons)
e. Packages completed during report period:	0	0	0
f. Packages completed to date:	0	0	0

6. Remarks:

Packaging completion date for substation and crane is 20 Nov 49.

E. Urakami
Chief Custodian
7. Signature

8. Title

9. Reviewed by:

10. Signature

11. Title

DECLASSIFIED E.O. 12065 SECTION 3 (E), NARS

file
alloc. not
pack & crat

31 August 1949

Memo for Record -

1. As per telephone instructions from Miss Bull, KCAR, to Mr. Keisel, Netherlands and UK have waived final inspection of crated items by their resident engineers. Crates will be closed after inspection and approval by this headquarters.

R. A. S.

DECLASSIFIED E.O. 11652 Section 3(E), 5(D) or (E)

file
alloc not
pack. & civil.

HEADQUARTERS
OSAKA CIVIL AFFAIRS TEAM
APO 25

HCK/ras/lmp

20 August 1949

SUBJECT: Plan for Execution of Allocation Notices

TO : General Headquarters, Supreme Commander for the Allied Powers, APO 500
ATTN: Civil Property Custodian

1. Herewith transmitted are reports of plans for execution of Allocation Notices 1-68, 1-69, 2-60, 2-61, 3-60, 3-61, 4-63 and 4-65, all pertaining to the Osaka Arsenal, plant 32-32.

2. Cited reports were prepared and submitted to this headquarters by the Osaka Finance Division.

FOR THE CHIEF:

FRED N. ALEXANDER
WOJG USA
Asst Adjutant

4 Incls:
reports as above (ea quad)
1-Alloc. Not. 1-68 & 1-69
2- " " 2-60 & 2-61
3- " " 3-60 & 3-61
4- " " 4-63 & 4-65

OSAKA M.G.
RES-COMMAND
FILE 05742

KINKI

OSAKA LIAISON & COORDINATION OFFICE

Prefectural Building
OSAKA

TS/ts

KKLCO No. 701 ER

17 August 1949

TO : Chief,
Osaka Civil Affairs Team

SUBJECT: Report on Plan for Packing Operation of Reparation Removal at Osaka Aresnal (32-32)

1. Reference: Memorandum for Japanese Government from General Headquarters Supreme Commander for Allied Powers, AG, 387.6 (22 July 1947) REP (SCAPIN 1751) dated 22 July 1947.

2. In compliance with annex 1 of the reference memorandum, subject report ~~are~~ is submitted herewith.

3. For transmission to higher headquarters and for your information.

S. Shima
Director

Incl: Report as cited above prepared by the Osaka Finance Division.

OSAKA M.G
RES-COM-IND
FILE 1-5722

OSAKA FINANCE OFFICE
(Osaka)

15 August 1949

OFO No. 17

TO : Osaka Civil Affairs Team

SUBJECT: Report on Plan for Packaging Operation of Reparation Removal.

THRCUGH: Kinki Liaison and Coordination Office

1. We are submitting herewith the attached plan for packing operation of reparation removal in accordance with the memorandums, SCAPIN 5825-A/36, dated 20 June 1949 and SCAPIN 5825-A/40, dated 30 June 1949.

2. Regarding the detail of the machinery and equipments will be forwarded your headquarters at the earliest date.

FOR THE CHIEF OF OSAKA FINANCE OFFICE:

for H. Kumbaza
MITSUHARU, MATSUDA
Vice Chief,
Osaka Finance Office

REQUESTED CONDITION TO CARRY OUT THE REPARATIONS REMOVAL PROGRAM

Reparations removal of the Osaka Arsenal in accordance with the memorandums, SCAPIN 5825-A/36 and SCAPIN 5825-A/40, from the General Headquarters, Supreme Commander for the Allied Powers shall be carried out as the attached sheet.

However, the complete condition of the following points shall be required to carry out the program.

1. Collateral construction

   (1) Leaking of rain

   The complete prevention of the leaking of rain by repairing of the roof of the designated work shop shall be required, otherwise the program will not be carried out.

   (2) Repairing of cranes

   The cranes being damaged shall be repaired.

   (3) Centralization of the remaining machinery located in the work shop shall be required.

   (4) Road Repairing for transportation of Package, materials, and machinary

2. Exemption of cranes to be used and some transforming facilities from the program.

   Packaging and removal of the cranes and transforming facilities to be used for packaging and shipping shall be made after the completion of the program.

3. The packaged items shall be stored in the arsenal until the commencement of the transportation, and 30% out of them shall be

(1) Leaking of rain

The complete prevention of the leaking of rain by repairing of the roof of the designated work shop shall be required, otherwise the program will not be carried out.

(2) Repairing of cranes

The cranes being damaged shall be repaired.

(3) Centralization of the remaining machinery located in the work shop shall be required.

(4) Road Repairing for transportation of Package, materials, and machinery

2. Exemption of cranes to be used and some transforming facilities from the program.

Packaging and removal of the cranes and transforming facilities to be used for packaging and shipping shall be made after the completion of the program.

3. The packaged items shall be stored in the arsenal until the commencement of the transportation, and 30% out of them shall be centralized in the outdoor.

4. Actual operation from the commencement date of the operation.

At least four days of the preparation period shall be required after the anticipated commencement date of the operation, and it is required the contractors who are able to complete the estimated quantity designated by the Government.

5. Transportation and delivery of the materials to be used.

The transportation and delivery of the materials shall be made by the Osaka Special Procurement Board, required amount of materials indicated in the attached sheet to completely enforce the operation in accordance with the memorandum, SCAPIN 1751, shall be required.

The delivery of the materials to the contractors should be accorded to the period indicated in the attached chart.

6. Type of contract shall be accorded with the type of operation, operation shall be enforced strictly by the type of operation even in case a few types of operation amalgamately was contracted, and maximum capacity of the contract will be considered.

7. The items and the quantity exempted from this program are indicated as the attached sheet and packaging operation shall be carried out until November 30 upon the completion of the above program.

PLAN FOR REMOVAL OF INTEGRATED FACILITIES AND POOLED ITEM

OSAKA MILITARY ARSENAL
PLANT CODE NO. 32-32

ALLOCATION NOTICE NO	RECIPIENT NATION
1 - 68	CHINA
1 - 69	"
2 - 61	NETHERLAND
2 - 60	"
3 - 60	PHILIPPINES
	"

PLAN FOR REMOVAL OF INTEGRATED FACILITIES AND POOLED ITEM

1. Allocation Notice.

   a. Allocation Notice No. and Date: 1-68, 30 ~~July~~ June, 1-69, 30 ~~July~~ June

   b. Recipient Nation: China

   c. Received by Reparation Board on:

   d. Received by Local Liaison and Coordination Office on:

   Received by Osaka Financial Office on: 29 ~~July~~ June and 9 ~~June~~ July 1949

2. Plant Being Reported on:

   a. Plant Code No. 32-32

   b. Name of Plant: Osaka Military Arsenal

   c. Location: 1, Sugiyama-cho, Higashi-ku, Osaka City

   d. Industrial Category of Allocated Item: Arsenal

3. Removal Equipment (not including building)

   a. Net weight (metric ton) 5,699.057

   b. Gross weight(") 6,838,868

   c. Gross Volume(meas. ton) 13,677.736

   d. Total No. of Package 1385

   e. List of removal Equipment (Biggest and weightest as a Package)

Inv. No.	Name of Items or Component Parts	Size of Item or Component Parts

b. Name of Plant: Osaka Military Arsenal

c. Location: 1, Sugiyama-cho, Higashi-ku, Osaka City

d. Industrial Category of Allocated Item: Arsenal

3. Removal Equipment (not including building)

a. Net weight (metric ton) 5,699.057

b. Gross weight(") 6,838,868

c. Gross Volume(meas. ton) 13,677.736

d. Total No. of Package 1385

e. List of removal Equipment (Biggest and weightest as a Package)

Inv. No.	Name of Items or Component Parts	Size of Item or Component Parts Net Weight	Net Volume	Remarks
5165	Steam Jib Crane	42.500	7.0x2.7x5.5 103.95	
5165	"	42.500	7.0x2.7x5.5 103.95	

f. Outline of Dismantling of Chief Item:

~~See attached sheet No.~~

4. Time Required:

a. Time limit shown on allocation notice: None

b. Total time required: 31 Oct 1949 (However cranes and substation will take until 25 Nov 1949)

c. Gant Chart

See attached sheet No.2.

d) Order of removal:

1) Packaging of items in Allocation Notice No. 1-69 will be carried out upon the completion of packaging of items in Allocation Notice No. 1-68.

2) Start from the items in the packaging work shop and dismantling, cleaning and packaging will be carried out side of side.

e) Chart for entire removal operation:

See attached Chart.

5) Principal non expendable items requred for removal:

Item	Unit	Amount	Remarks
Gas Welder Mach	ea.	1	
Electric Winch	ea.	2	
Chain Block	ea.	3	
Manila Rope	m.	200	
Wire Rope	m.	50	
Circular Saw	ea.	5	
Balance	ea.	3	
Trailer	ea.	20	
Track	ea.	850	
Wagen	ea.	500	

Electric Winch	ea.	2
Chain Block	ea.	3
Manila Rope	m.	200
Wire Rope	m.	50
Circular Saw	ea.	5
Balance	ea.	3
Trailer	ea.	20
Track	ea.	850
Wagon	ea.	500
Electric Drill	ea.	12
Electric Wire	m.	200

6) Principal expendable items required for removal:

Item	Unit	Amount	Per ton	Remark
Lumber	kcbm	14817	2.6	
Wooden Wool	kg	1709	0.3	
Steel Plate	"	13107	2.3	
Corner Strap	"	4559	0.8	
Steel Band	"	3989	0.7	
Nail	"	39893	5.0 ~~0.03~~	
Nail (roofing)	"	17097	0.03	
Washer Roofing	"	17097	0.03	
Bolt and Nut	"	28495	5.0	

I tem

Item	Unit	Amount	Per ton	Remark
Wire	kg	1,139.8	0.2	
Lag Screw	"	2,279.6	0.4	
Carbide	"	2,849.5	0.5	
Oxygen	Cub. m	1,139.8	0.2	
Paint, Preservative	kg	284.95	0.05	
Cool-tar	"	569.9	0.1	
Solvent	"	113.98	0.02	
Waste	"	3,419.4	0.6	
Asphalt roofing	Cub. m.	740.87	0.13	
Asphalt felt	"	3,704.35	0.65	
Sand Paper	Sheet	3,419.4	0.60	
Gasoline	lt.	1,139.8	0.20	
Kerosen or light oil	"	5,699	1.0	
Machine oil	"	1,709.7	0.3	
Oil Lubricating	"	1,139.8	0.2	
Grease	kg	2,849.5	0.5	
Paper for Packing list	Sheet	1,424.75	25	
Envelope for Packing list	"	7,408.7	1.3	

Waste	"	3,419.4	0.6
Asphalt roofing	Cub. m.	740.87	0.13
Asphalt felt	"	3,704.35	0.65
Sand Paper	Sheet	3,419.4	0.60
Gasoline	lt.	1,139.8	0.20
Kerosen or light oil	"	5,699	1.0
Machine oil	"	1,709.7	0.3
Oil Lubricating	"	1,139.8	0.2
Grease	kg	2,849.5	0.5
Paper for Packing list	Sheet	1,424.75	25
Envelope for Packing list	"	7,408.7	1.3

(7) Other note (Including special instruction shown in allocation notice)

None

(8) Date of special construction for removal work

(1) Repairing Construction (Preventing the leaking of rain at the packaging work shop)

Repairing Expenses for 6,600 sq.m.....¥ 3,000,000.--

(2) Repairing Work for Cranes

Repairing Expenses for Nine Cranes.....¥ 265,000.--

(3) Centralization and Orderliness of the Remaining Machinery in the packaging work shop.

1775 Machines (4535 tons).....¥ 1,690,000.--

GANT CHART

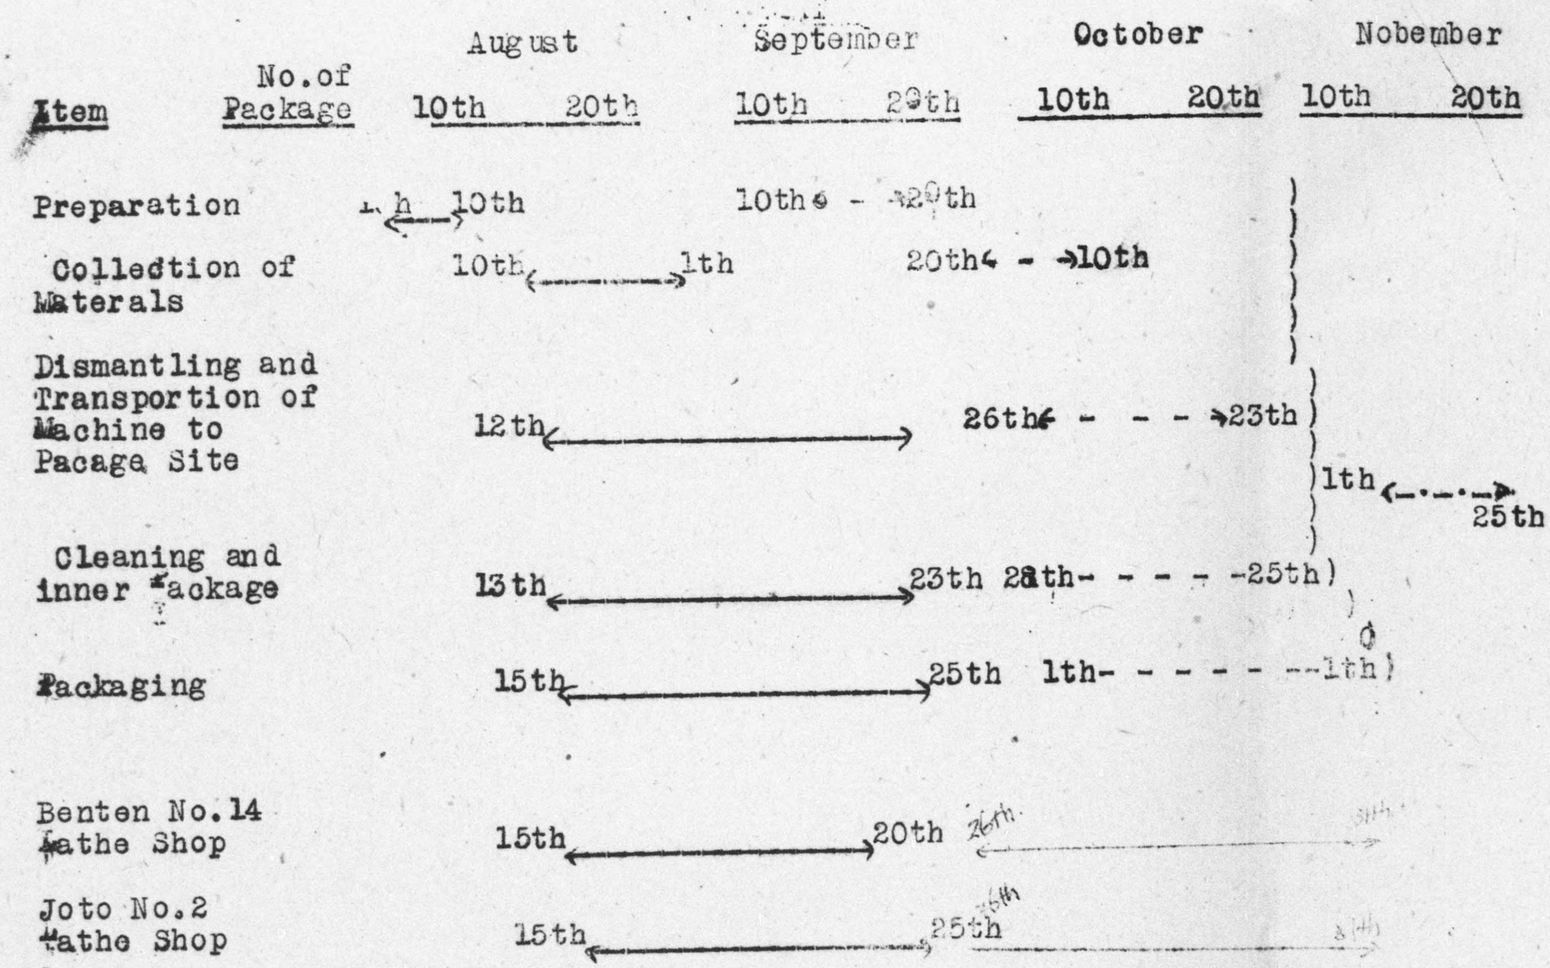

Note:

For Allocation Notice No. 1-68. ←——→

\- " - No. 1-69 ←- - - - - →

For the Cranes used for packing operation indicates ←.-.-.-.-→

PLAN FOR REMOVAL OF INTEGRATED FACILITIES AND POOLED ITEM

1. Allocation Notice.

   a. Allocation Notice No. and Date: 2-61, 20 July. 2-60, 30 July

   b. Recipient Nation: Netherland

   c. Received by Reparation Board on: _____

      Received by Local Liaison and Coordination Office on: _____

      Received by Osaka Finance Office on: 29 ~~July~~ June and 9 ~~June~~ July 1949

2. Plant Being Reported On:

   a. Plant Code No. 32-32

   b. Name of Plant: Osaka Military Arsenal

   c. Location: 1, Sugiyama-cho, Higashi-ku, Osaka City

   d. Industrial Category of Allocated Item: Arsenal

3. Removal Equipment (not including building)

   a. Net weight (metric ton) 243.123

   b. Gross weight(") 291.847

   c. Gross Volume(meas ton) 337.77

   d. Total no.of Package 152

   e. List of removal Equipment (Bigest and Weightest as a Package)

c. Location: 1, Sugiyama-cho, Higashi-ku, Osaka City

d. Industrial Category of Allocated Item: Arsenal

3. Removal Equipment (not including building)

a. Net weight (metric ton) 243.123

b. Gross weight(") 291.847

c. Gross Volume(meas ton) 337.77

d. Total no.of Package 152

e. List of removal Equipment (Bigest and Weightest as a Package)

Inv. No.	Name of Items or Component Parts	Size of Item or Component Parts Net Weight	Net Volume	Remark
470	Overhead Travelling Crane	8,500	20.0xl.5xl.5 45.0	
470	"	"	"	

f. Outline of Dismantling of Chief Item

See attached sheet No.1.

4. Time Required:

a. Time limit shown on allocation Notice: None

b. Total time required: 5 Oct 1949 (However cranes will take until 25 Nov 1949)

c. Gant Chart:

See attached sheet No.2.

d) Order of removal

1) Packaging of items in Allocation Notice No. 2-60 will be carried out upon the completion of packaging of items in Allocation Notice No. 2-61.

2) Start from the items in the packaging work shop and dismantling, cleaning and packaging will be carried out side by side.

e) Chart for entire removal operation.

See attached Chart.

5) Principal non expendable items required for removal.

Item	Unit	Amount	Remarks
Electric Winch	ea.	1	
Chain Block	ea.	2	
Manila Rope	m.	100	
Circular Saw	ea.	2	
Balance	ea.	2	
Track	ea.	20	
Wagon	ea.	25	
Electric Drill	ea.	2	
Electric Wire	m.	100	

6) Principal expendable Items required for removal:

Item	Unit	Amount	Per ton	Remarks

Electric Winch	ea.	1
Chain Block	ea.	2
Manila Rope	m.	100
Circular Saw	ea.	2
Balance	ea.	2
Track	ea.	20
Wagon	ea.	25
Electric Drill	ea.	2
Electric Wire	m.	100

6) Principal expendable Items required for removal:

Item	Unit	Amount	Per ton	Remarks
Lumber	koku	631.8	2.6	
Wooden Wool	kg.	72.9	0.3	
Steel Plate	"	558.9	2.3	
Corner Strap	"	194.4	0.8	
Steel band	"	169.1	0.7	
Nail	"	1,701	7.0	
Nail (roofing)	"	7.29	0.03	
Washer roofing	"	7.29	0.03	
Bolt and Nut	"	1,315	5.0	

Item	Unit	Amount	Per ton	Remark
Wire	kg	48.6	0.2	
Lag Screw	"	1,555.2	0.4	
Carbide	"	131.5	0.5	
Oxygen	Cub. m	48.6	0.2	
Paint, Preservative	kg	13.15	0.05	
Coal- tar .	"	24.3	0.1	
Solvent	"	4.86	0.02	
Waste	"	145.8	0.6	
Asphalt roofing	Cub.m.	315.9	0.13	
Asphalt felt	"	1,579.5	0.65	
Sand Paper	Sheet	145.8	0.60	
Gasoline	lt.	48.6	0.2	
Kerosen or light oil	"	243	1.0	
Machine oil	"	72.9	0.3	
Oil Lubricating	"	48.6	0.2	
Grease	kg	131.5	0.5	
Paper for Packing list	Sheet	6,075	25	
Envelope for Packing list	"	3,159	1.3	

(7) Other note (Including special instruction shown in allocation notice)

Solvent	"	4.86	0.02
Waste	"	145.8	0.6
Asphalt roofing	Cub.m.	316.9	0.13
Asphalt felt	"	1,579.5	0.65
Sand Paper	Sheet	145.8	0.60
Gasoline	lt.	48.6	0.2
Kerosen or light oil	"	243	1.0
Machine oil	"	72.9	0.3
Oil Lubricating	"	48.6	0.2
Grease	kg	131.5	0.5
Paper for Packing list	Sheet	6,075	25
Envelope for Packing list	"	3,159	1.3

(7) Other note (Including special instruction shown in allocation notice)

None

(8) Date of special construction for removal work

(1) Repairing Construction (Preventing the leaking of rain at the packaging work shop)

Repairing Expenses for 6,000 Sq.M.....¥ 3,000,000.--

(2) Repairing Work for Cranes

Repairing Expenses for Nine Cranes.....¥ 265,000.--

(3) Centralization and Orderliness of the Remaining Machinery in the Packaging Work Shop.

1775 Machines (4535 tons).....¥ 1,690,000.--

GANT CHART

Item	No. of Package	August 10th	August 20th	September 10th	September 20th	October 10th	October 20th	November 10th	November 20th
Preparation		1th ←——→	15th	5th← - -	→15th				
Collection of Materals		10th ←——→	25th	10th← - -	→30th				
Dismantling and Transportion of Package Site.			17th ←——→	10th	15th← - -	→1th			
								1th ←-.-.-.-.-→	25th
Cleaning and inner Package			17th ←——→	12th	16th← - -	→1th			
Packaging			18th ←——→	15th	16th← - - -	→5th			
Adjusment of Packago				10th ←——→	15th	1th← - -	→5th		
Joto Pattern Shop			17th	15th	16th← - - -	→5th			

Noto:

For the Allocation Notico No.2-61 indicates. ←——→

- " - No.2-60 indicates ← - - - - - - - →

For the Cranes used for packing operation indicates ←-.-.-.-.-.-→

PLAN FOR REMOVAL OF INTEGRATED FACILITIES AND POOLED ITEM

1. Allocation Notice.

   a. Allocation Notice No. and Date: 3-60, 20 ~~July~~ June. 3-61, 30 ~~July~~ June

   b. Recipient Nation: Philippines

   c. Received by Reparation Board on: _____

      Received by Local Liaison and Coordination Office on: _____
      Received by Osaka Financial Office on: 29 July and 9 June 1949.
      June July

2. Plant Being Reported On:

   a. Plant Code No. 32-32

   b. Name of Plant: Osaka Military Arsenal

   c. Location: 1, Sugiyama-cho, Higashi-ku, Osaka City

   d. Industrial Category of Allocated Item: Arsenal

3. Removal Equipment (Not including building)

   a. Net Weight (metric ton) 3,344.724

   b. Gross Weight(") 4,013.668

   c. Gross Volume(meas.ton) 8,027.336

   d. Total No. of Package: 1,240

   e. List of Removal Equipment (Bigest and weight ~~as a Package~~)

Inv. No.	Name of Items or Component Parts	Size of Item or Component Parts		Remark
		Net Weight	Net Volume	
1691	Cylinder for	45.000 Kg.	7.0x2.5x2.5	

Received by Osaka Financial Office on: 29 May and 5 June July

2. Plant Being Reported On:

a. Plant Code No. 32-32

b. Name of Plant: Osaka Military Arsenal

c. Location: 1, Sugiyama-cho, Higashi-ku, Osaka City

d. Industrial Category of Allocated Item: Arsenal

3. Removal Equipment (Not including building)

a. Net Weight (metric ton) 3,344.724

b. Gross Weight(") 4,013.668

c. Gross Volume(meas.ton) 8,027.336

d. Total No. of Package: 1,240

e. List of Removal Equipment (Bigest and weightest as a Package)

Inv. No.	Name of Items or Component Parts	Size of Item or Component Parts Net Weight	Net Volume	Remark
1691	Cylinder for Hydroric Press	45.000 Kg.	7.0x2.5x2.5 43.7	
1691	"	45,000	7.0x2.5x2.5 43.7	

f. Outline of Dismantling of Chief Item

See attached sheet No.1.

4. Time Required:

a. Time limit shown on allocation notice: None

b. Total time required: October 31, 1949 (Crane and substation ....to November 25, 1949)

x. Gant Chart:

See attached sheet No.2.

d) Order of removal:

1) Packaging of items in Allocation Notice No. 3-61 will be carried out upon the completion of packaging of items in Allocation Notice No. 3-60.

2) Start from the items in the packaging work shop and dismantling, cleaning and packaging will be carried out side by side.

e) Chart for entire removal operation:

See attached Chart.

5) Principal non expandable items required for removal.

Item	Unit	Amount	Remarks
Electric Winch	ea.	1	
Chain Block	ea.	3	
Manila Rope	m.	150	
Wire Rope	m.	50	
Circular Saw	ea.	3	
Balance	ea.	2	
Trailer	ea.	10	
Track	ea.	350	
Wagon	ea.	300	
Electric Drill	ea.	3	
Electric Wire			

Item	Unit	Amount	Remarks
Electric Winch	ea.	1	
Chain Block	ea.	3	
Manila Rope	m.	150	
Wire Rope	m.	50	
Circular Saw	ea.	3	
Balance	ea.	2	
Trailer	ea.	10	
Track	ea.	350	
Wagon	ea.	300	
Electric Drill	ea.	3	
Electric Wire	m.	250	

6) Principal expendable items required for removal.

Item	Unit	Amount	Per ton	Remarks
Lumber	koku	9696	2.6	
Wooden Wool	kg.	1003	0.3	
Steel Plate	"	7692	2.3	
Corner Strap	"	2675	0.8	
Steel band	"	~~2675~~ 3760	0.7	
Nail (Common)	"	23408	7.0	
Nail (roofing)	"	100	0.03	
Washer roofing	"	120	0.03	
Bolt and Nut	"	1672	5.0	

Item	Unit	Amount	Per Ton	Remark
Wire	kg	668.8	0.2	
Lag Screw	"	1,337.6	0.4	
Carbide	"	1,672.		
Oxygen	Cub. m	668.8	0.2	
Paint,Preservative	kg	167.2	0.05	
Cool-tar	"	334.4	0.1	
Solvent	"	66.88	0.02	
Waste	"	2,006.4	0.6	
Asphalt roofing	Cub. m.	434.72	0.13	
Asphalt felt	"	2,173.60	0.65	
Sand Paper	Sheet	2,006.4	0.60	
Gasoline	lt.	668.80	0.20	
Kerosen or light oil	"	3,344	1.0	
Machine oil	"	1,003.2	0.3	
Oil Lubricating	"	668.8	0.2	
Grease	kg	1,672.	0.5	
Paper for Packing list	Sheet	82.600	25	
Envelope for Packing list	"	4,347.2	1.3	

Waste	"	2,006.4	
Asphalt roofing	Cub. m.	434.72	0.13
Asphalt felt	"	2,173.60	0.65
Sand Paper	Sheet	2,006.4	0.60
Gasoline	lt.	668.80	0.20
Kerosen or light oil	"	3,344	1.0
Machine oil	"	1,003.2	0.3
Oil Lubricating	"	668.8	0.2
Grease	kg	1,672.	0.5
Paper for Packing list	Sheet	82.600	25
Envelope for Packing list	"	4,347.2	1.3

(7) Other note (Including special instruction shown in allocation notice)

None

(8) Date of special construction for removal work.

(1) Repairing Construction (Preventing the leaking of rain at the packaging work shop)

Repairing Expenses for 6,600 sq. m..... ¥ 3,000,000.--

(2) Repairing Work for Cranes

Repairing Expenses for Nine Cranes..... ¥ 265,000.--

(3) Centralization and Orderliness of the Remaining Machinery in the Packaging Work Shop.

1775 machines (4535 tons)..... ¥ 1,690,000.--

GANT CHART

Item	No. of Package	August 10th	August 20th	September 10th	September 20th	October 10th	October 20th	Nobemb 10th	Nobemb 2
Preparation		1th ⟷ 11th		5th ← - → 20th		25th ⟷ 8th			
Collection of Materals		10th ⟷		5th	15th ← - - → 10th		1th ⟷	10t	
Dismantling and Transportion of Machine to Package Site		12 th ⟷		15th	26th ← - → 20th	1th ⟷		15t	
Cleaning and inner Package		14th ⟷		18th	27th ← - → 25th	3th ⟷		18	
Packaging		15th ⟷		20th	27th ← - - - → 1th	5th ⟷		25	
Adjusment of Package	4			15th ⟷ 25th		20th ← - → 1th			
Bonten No. 14 Lathe Shop		15th ⟷		20th	26th ← - - - - - - → 1th				
Bonten No. 2 Lathe Shop		17th ⟷		18th					
Joto No. 1 Lathe Shop		15th ⟷		20th					

Note :

For the Allocation Notice No. 3-60 indicates ⟷

Materals	10th ⟵——⟶ 5th 15th ⟵ - - → 10th 1th ⟵._.⟶ 10t
Dismantling and Transportion of Machine to Package Site	12 th ⟵——⟶ 15th 26th ⟵ - → 20th 1th ⟵._.⟶ 15t
Cleaning and inner Package	14th ⟵——⟶ 18th 27th ⟵ - → 25th 3th ⟵._.⟶ 18
Packaging	15th ⟵——⟶ 20th 27th ⟵ - - - → 1th 5th ⟵._.⟶ 25
Adjusment of Package	15th ⟵——⟶ 25th 20th ⟵ - → 1th
Benten No. 14 Lathe Shop	15th ⟵——⟶ 20th 26th ⟵ - - - - - - → 1th
Benten No. 2 Lathe Shop	17th ⟵——⟶ 18th
Jeto No. 1 Lathe Shop	15th ⟵——⟶ 20th

Note :

For the Allocation Notice No. 3-60 indicates ⟵——⟶

- " - No. 3-61 indicates ⟵ - - - - - →

For the Cranes and substation used for packing operation indicates ⟵.-.-.-.⟶

PLAN FOR REMOVAL OF INTEGRATED FACILITIES AND POOLED ITEM

1. Allocation Notice.

   a. Allocation Notice No. and Date: 4-63, 20 ~~July~~ June. 4-65, 30 July June

   b. Recipient Nation: _____

   c. Received by Reparation Board on: _____
      Received by Local Liaison and Coordination Office on:
      Received by Osaka Financial Office on: 29 July and 9 June 1949.
      June July

2. Plant Being Reported on:

   a. Plant Code No. 32-32

   b. Name of Plant: Osaka Military Arsenal

   c. Location: 1 Sugiyama-cho, Higashiku, Osaka City

   d. Industrial Category of Allocated Item: Arsenal

3. Removal Equipment (not including building)

   a. Net weight (metric ton) 7,696.985

   b. Gross weight(") 9,236.472

   c. Gross volume(meas.ton) 21,243.685

   d. Total No. of Package 1,190

   e. List of removal Equipment (Biggest and Weightest as a package).

Inv. No.	Name of Items or Component Parts	Size of Item or Component Parts Net Weight	Net Volume	Remark
6251	Boiler (Dram)	14.000	8.5x1.9x3.6	

a. Plant Code No. 32-05

b. Name of Plant: Osaka Military Arsenal

c. Location: 1 Sugiyama-cho, Higashiōku, Osaka City

d. Industrial Category of Allocated Item: Arsenal

3. Removal Equipment (not including building)

a. Net weight (metric ton) 7,696.985

b. Gross weight(") 9,236.472

c. Gross volume(meas.ton) 21,243.685

d. Total No. of Package 1,180

e. List of removal Equipment (Bigest and Weightest as one package).

Inv. No.	Name of Items or Component Parts	Size of Item or Component Parts Net Weight	Net Volume	Remark
5251	Boiler (Drum)	14.000	8.5x1.9x3.6 58.13	
5405	Steam Hammer(Anvil)	55.000	5.0x3.0x0.3 45	

f. Outline of Dismantling of Chief Item:

See attached sheet No.1.

4. Time Required:

a. Time limit shown on allocation Notice: None

b. Total time required: 31 Oct 1949 (However cranes and substation will take until 25 Nov 1949)

c. Gant Chart:

See attached sheet No.3.

Item	Unit	Amount	Perton	Remarks
Wire	kg	1,539.2	0.2	
Lag Screw	"	3,078.4	0.4	
Carbide	"	3,848.	0.5	
Oxygen	Cub. m.	1,539.2	0.2	
Paint, Preservative	kg	384.8	0.05	
Cool- tar	"	769.6	0.1	
Solvent	"	153.92	0.02	
Waste	"	4,617.6	0.6	
Asphalt roofing	Cub. m.	1,000.48	0.13	
Asphalt felt	"	5,002.4	0.65	
Sand Paper	Sheet	4,617.6	0.60	
Gasoline	lt.	1,539.2	0.2	
Kerosen or light oil	"	7,696.	1.0	
Machine Oil	"	2,308.8	0.3	
Oil Lubricating	"	1,539.2	0.2	
Grease	kg	3,848.	0.5	
Paper for Packing list	Sheet	192,400	25	
Envelope for Packing list	"	10,004.8	1.3	

Asphalt roofing	Cub. m.	1,000.48	0.13
Asphalt felt	W	5,002.4	0.65
Sand Paper	Sheet	4,617.6	0.60
Gasoline	lt.	1,539.2	0.2
Kerosen or light oil	"	7,696.	1.0
Machine Oil	"	2,308.8	0.3
Oil Lubricating	"	1,539.2	0.2
Grease	kg	3,848.	0.5
Paper for Packing list	Sheet	192,400	25
Envelope for Packing list	"	10,004.8	1.3

(7) Other note (Including special instruction shown in allocation notice)

None

(8) Date of special construction for removal work.

( ) (1) Repairing Construction (Preventing the leaking of rain at the packaging work shop)

Repairing Expenses for 6,600 sq. m.....¥ 3,000,000.--

(2) Repairing Work for Cranes

Repairing Expenses for Nine Cranes.....¥ 265,000.--

(3) Centralization and Orderliness of the Remaining Machinery in the Packaging Work Shop

1775 Machines (4535 tons).....¥ 1,690,000.--

d) Order of removal:

1) Packaging of items in Allocation Notice No. 4-65 will be carried out upon the completion of packaging of items in Allocation Notice No. 4-63.

2) Start from the items in the packaging work shop and dismantling, cleaning and packaging will be carried out side by side.

e) Chart for entire removal operation.

See attached Chart.

5) Principal non expendable items required for removal.

Item	Unit	Amount	Remarks
Electric Winch	ea.	2	
Gas Welder	ea.	1	
Chain Block	ea.	3	
Manila Rope	m.	200	
Wire Rope	m.	50	
Circular Saw	ea.	6	
Balance	ea.	3	
Trailer	ea.	15	
Track	ea.	1000	
Wagon	ea.	1000	
Electric Drill	ea.	10	
Electric Wire	m.	250	

Electric Winch	ea.	2
Gas Welder	ea.	1
Chain Block	ea.	3
Manila Rope	m.	200
Wire Rope	m.	50
Circular Saw	ea.	6
Balance	ea.	3
Trailer	ea.	15
Track	ea.	1000
Wagon	ea.	1000
Electric Drill	ea.	10
Electric Wire	m.	250

6) Principal expendable Items required for removal.

Item	Unit	Amount	Per ton	Remarks
Lumber	koku	2002.1610	2.6	
Wooden Wool	kg.	2309.0955	0.3	
Steel Plate	kg.	17703.0655	2.3	
Corner Strap	"	6157.5880	0.8	
Steel Band	"	5387.8895	0.7	
Nail	"	53878.8950	7.0	
Nail (roofing)	"	230.90955	0.03	
Washer roofing	"	230.90955	0.03	
Bolt and Nut	"	3848.4925	5.0	

GANT CHART

Item	No.of Package	August 10th	August 20th	September 10th	September 20th	October 10th	October 20th	November 10th	November 20th
Preparation		1th ⟷ 10th		11th ⟷ 14th					
Collection of Materals		10th ⟷ 5th		15th ⟷ 10th					
Dismantling and Transportion of Machine to Package Site		12th ⟷	15th	20th ⟷	20th				
Cleaning and inner Package		14th ⟷	17th	22th ⟷	25th				
Packaging		15th ⟷	21th	25th ⟷	1th				
Adjusment of Package		15th ⟷	21th	20th ⟷	1th				
Benten No. 14 Lathe Shop		15th ⟷						1th	
Benten No.2 Lathe Shop		26th ⟷						1th	

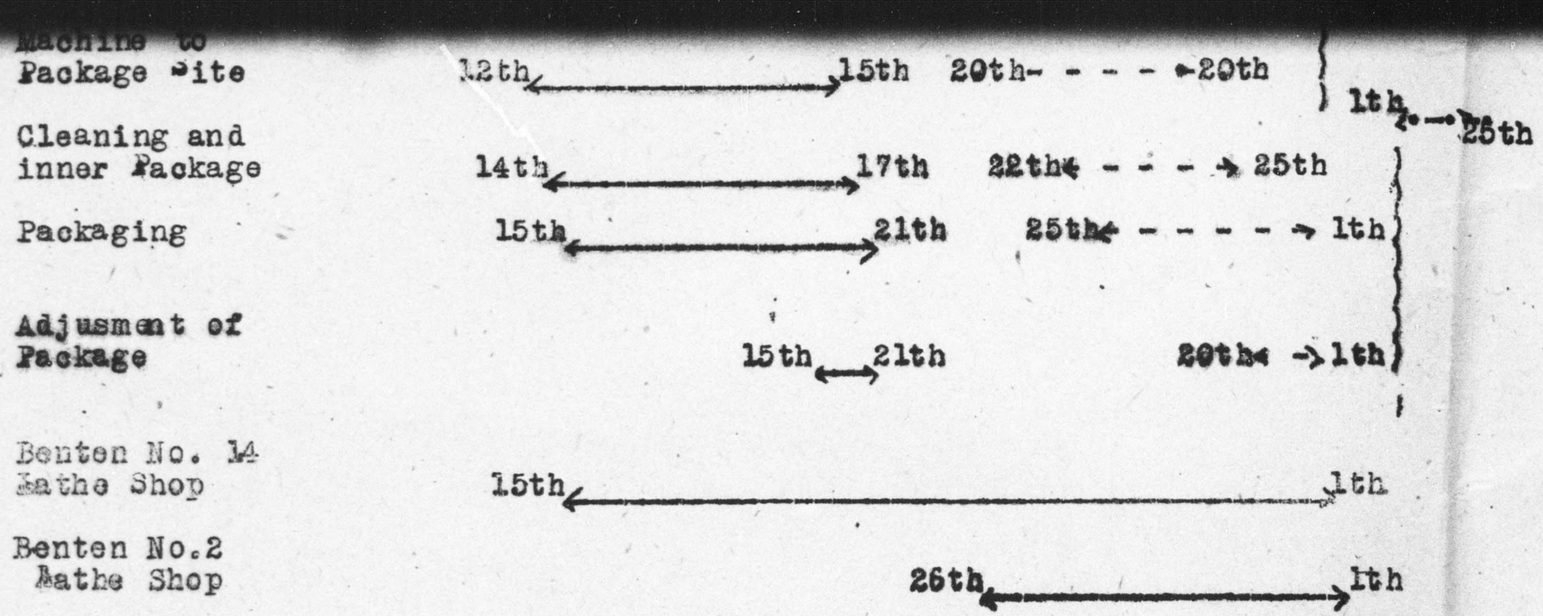

Note:

For the Allocation Notice No. 4-63 indicates. ←——→

- " - No. 4-65 indicates ←- - - →

For the Cranes used for packaging operation indicates. ←·-·-·-·→

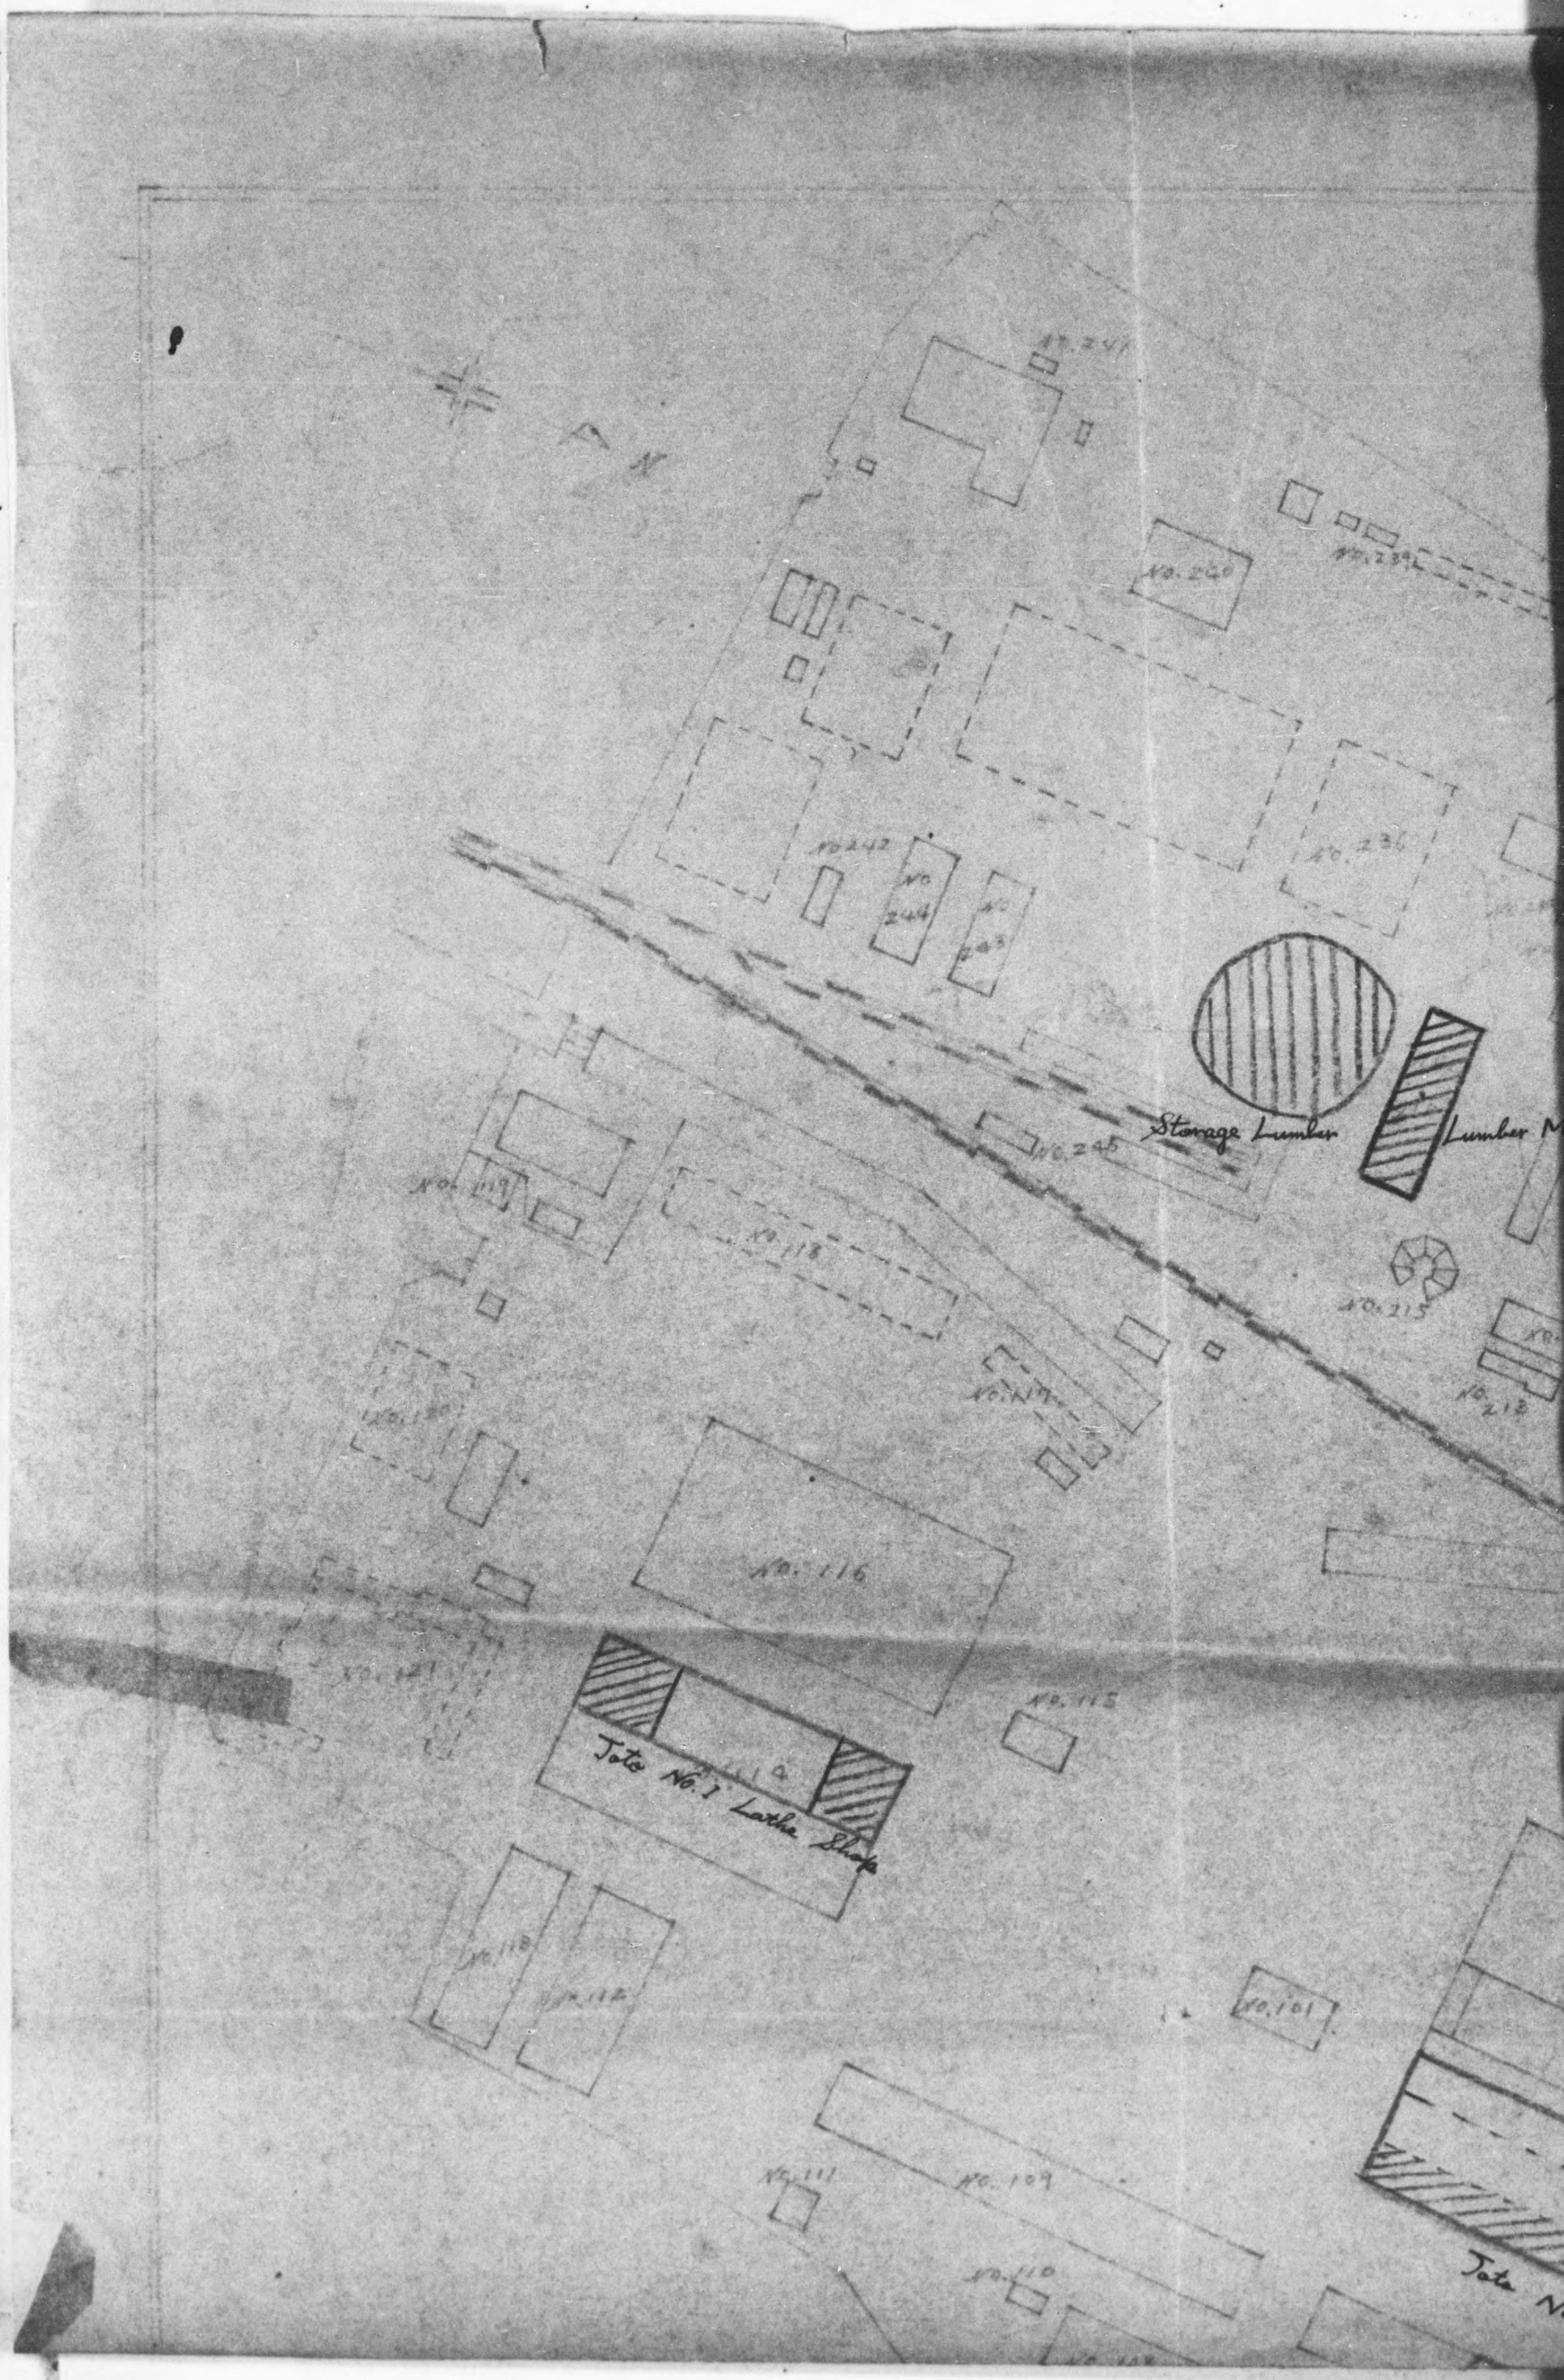
N
No. 241
No. 240
No. 239
No. 242
No. 244
No. 243
No. 236
Storage Lumber
Lumber M
No. 245
No. 119
No. 118
No. 117
No. 120
No. 121
No. 116
No. 115
No. 215
No. 213
Tote No. 1 Lathe Shop
No. 114
No. 113
No. 112
No. 111
No. 109
No. 110
No. 101
Tote No. 2
